#### U. S. NAVAL MOBILE CONSTRUCTION BATTALION SIXTY-TWO Care of Fleet Post Office New York 09501

MCB-62:CPO:mdb 5213 Ser: JUN 03 1967

From: Commanding Officer, U. S. Naval Mobile Construction Battalion SIXTY-TWO, FPO New York 09501

To: Commander, Naval Construction Battalions, U. S. Pacific Fleet, FPO San Francisco 96610

Operations Report for Period Ending 25 May 1967; submission of

Ref: (a) COMCBPAC INST 5213.1C (b) COMCBPAC OPORD 24-66

Encl: (1) Administrative Summary

(2) Equipment Status Report (3) Training Report

(4) Labor Distribution Report (5) Construction Item Summary

(6) Progress & Performance Chart

√(7) Fiscal Summary

(8) Progress Photographs (Black and White)

V(9) Color Slides (not included)

- In accordance with reference (a), MCB SIXTY-TWO's Operations Report is submitted for 26 April 1967 to 25 May 1967.
- 2. Employment Status. In accordance with reference (b), U. S. Naval Mobile Construction Battalion SIXTY-TWO is deployed to Hue Phu Bai. primary mission of the Battalion is construction in support of the 30th Naval Construction Regiment. The following unit is detached:

Seabee Team 6201: Deployed to CBC, Gulfport

- 3. Unit Movement. On 22 May 1967, Seabee Team 6201, comprised of one officer (LTJG. D.B. HERRMANN, CEC, USNR) and 12 men departed Phu Bai to return to CBC, Gulfport, for a period of leave and to commence training on 1 July 1967.
- 4. Significant Events.
  - The formation and departure of Seabee Team 6201. a.
- b. During the reporting period, MCB SIXTY-TWO was visited by the following persons:

CAPT A.R. MARSCHALL, CEC, USN, COMMODORE, 30NCR CAPT. H.J. JOHNSON, CEC, USN, DEPUTY COMMANDER PACDIV. NAVFACENGCOM

4 May: MAJ. HUNTZINGER, USMC, BASE DEVELOPMENT, DANANG

8 May: BRIG. GEN. M.E. GATES, USA, CORPS OF ENGINEERS,
MACV DIRECTOR OF CONSTRUCTION
COL. EGBERT, USA, CORPS OF ENGINEERS, MACV
DIRECTOR OF CONSTRUCTION
CDR. T.K. JONES, CEC, USN, MACDC
LCDR. R.P. WILKING, CEC, USN, MACDC
CAPT. A.R. MARSCHALL, CEC, USN, COMMODORE, 30NCR
CDR. R.F. JORTBERG, CEC, USN, CSO, 30NCR

9 May: CAPT. A.R. MARSCHALL, CEC, USN, COMMODORE, 30NCR CDR. R.D. KEEGAN, CEC, USN, C.O. MCB-6 CDR. R.D. COUGHLIN, CEC, USN, C.O. MCB-71

12 May: CAPT. C.G. MILLER, CEC, USN, CSO, CBPAC LCDR. F.M. NEWCOMB, CEC, USN, CBPAC

14 May: LT. P.L. GLEMAN, CEC, USN, NSA LT. M.M. COOPER, CEC, USN, NSA

20 May: CDR. D.A. BARTLEY, CEC, USN, C.O. MCB-10 LCDR. J.R. DUNN, CEC, USN, OPERATIONS OFFICER, MCB-10

23 May: CAPT. A? R. MARSCHALL, CEC, USN, COMMODORE, 30NCR CDR. J.W. TOMBARGE, CEC, USN, OPERATIONS OFFICER, 30NCR CDR. R.F. JORTBERG, CEC, USN, CSO, 30NCR CDR. C.C. HEID, CEC, USN, RELEIVING CSO, 30NCR CAPT. C.J. MERDINGER, CEC, USN, PWO, NSA LTJG. N.W. LUTTRELL, CEC, USNR, ENGINEERING OFFICER MCB-58

J.D. IRETON, METCALF & EDDY, OICC SOILS ENGINEER
27 May: J.D. IRETON, METCALF & EDDY, OICC SOILS ENGINEER

c. During this period the following major projects were completed:

6DSA55019

A-MED SECOND ADDITION

6ANA72528A 6APA72558A MCB 62-106E

SIXTH INCREMENT, 3RD MARDIV CANTONMENT

6DRA72306A

3RD MARDIV, MISC. CONSTRUCTION

d. MCB-3 has arrived in the Phu Bai area, establishing their camp at Gia Le. This makes two battalions in this area.

- 5. Major Problems. None
- 6. Significant Events Planned. None

W.J. RICHESON

#### Copy to: (With enclosures except as indicated)

```
NAVFACENGCOMD (CODE 50) (2) (less encl.(9))
CINCPACFLT (1) (less encl.(9))
COMSERVPAC (1) (less encl. (9))
COMSERLANT (1) (less encl. (9))
COMCBLANT (2)
COM3ONCB (1)
2ONCR (2) (Less encl. (9))
3ONCR (1) (less encl. (9))
CO, CBCEN, PORHUE (2) (less encl.(9))
CO NAVSCOLCONST (1) (less encl. (9))
CO NCEL (1) (less encl. (9))
CO NAVSCOL CEC OFF (1) (less encl. (9))
Dir of NAVAL HISTORY (1) (less encl. (9))
CG FMFPAC (1) (less encl. (9))
CG III MAF (2) (less encl. (9))
ALL NMCB's (1 each) (less encl 8) (less encl. (9))
CO NMCB One Hundred Twenty One (1) (less encl. (9))
CG 3RD MARDIV (1) (less encl. (9))
```

#### ADMINISTRATIVE SUMMARY

#### UNIT NMCB SIXTY-TWO

ADMINISTRATIVE SUMMARY FOR 26 APR 67 to 25 MAY 67.

#### 1. Personnel summary as of 25 May 1967.

	ON BOARD AT DEPLOY-	ATTACHED BUT NOT AT DEPLOY-	TOTAL PERSONNEL	CHANGES PER	
	MENT SITE	MENT SITE	ASSIGNED	RECEIPTS	TRANSFERS
E-9	1	0	1	0	0
E-8	5	0	5	0	0
E-7	32	6	38	0	0
E-6	68	7	75	1	0
E-5	117	27	144	0	1
E-4	286	3	289	3	14
Nonrated	263	0	263	6	14
Totals	772	43	815	0	0
Officers	22	1	23	0	0

				REAR	•				• •
	DETA1	L	TEAMS	ECHELON	PARTY	SCHOOLS	HOSP	BRIG	LEAVE
Office	er	0	1	0	0	0	0	0	0
Enlist	ed	0	12	31	0	0	0	0	0

### 2. Reenlistments.

- a. Separations eligible for reenlistment 9. Career 0. Non-career 9
- b. Reenlistments 1. Career 1. Non-career 0.
- c. Not recommended for reenlistment <u>O</u>. Career <u>O</u>. Non-career <u>O</u>.
- d. Personnel receiving separation interviews 190 .

## 3. Safety

#### a. Monthly Accident Summary

	ON DUTY	OFF DUTY	MANDAYS LOST	\$ DAMAGES
FIRST AID	6	0	N/A	N/A
LOST TIME	1	1	34	N/A
VEHICLE	0	0	N/A	0

- b. Total number of assigned automotive vehicles 104 Miles driven 65,866
- c. Stand-up safety meetings 33.

## 4. Discipline.

Number of cases heard at Captain's Mast 9; awarded NJP 9; Awarded Court-Martial 0.

## 5. Morale.

- a. Overall morale remains excellent. During the month two company beach parties were arranged for Colco Beach and a Sunday afternoon city of Hue guided tour program was initiated.
- b. Berthing provided by NMCB-62; condition good. All personnel now have bunks and mattresses which measurably improved berthing facilities.
  - c. Messing provided by NMCB-62; condition remains overall outstanding.

## 6. Medical/Dental.

- a. Total patients treated at sick call 633.
- b. Number Hospitalized 6.
- c. On sick list at end of period 0 .
- d. Dental patients treated 353.
- e. Total dental procedures 1136
- f. Number of personnel in each dental classification:

Class 1 - 292 Class 2 - 381

Class 3 - 88 Class 4 - 17

Class 5 - 2

2

ENCLOSURE (1)

	h.	Number of new VD cases 6. Total number 27. (Last month's report indicated total number of have read 21; the other cases reported were tho other command).	31 . It should se treated from
	i.	Total prescriptions filled 95.	
7.	Cha	plin Activities.	
9	a.	Number of services 3 PROTESTANT	
	ъ.	Average attendance 430 27	
	c.	Religious training classes _5.	
	d.	Red Cross 9.	
8.	Pub	lic Relations.	
	a.	FHTNC releases 5.	
	b.	Other Media releases 4 to 30 outlets.	
	c.	Newspaper issues published 2.	
	d.	Family grams 1.	
9.	Awa	rds & Promotions, live destisory procedures accomp	lished .279
	a.	Promoted to E-7 6 . Total number _27 .	** ***
	b.	Promoted to E-6 1 1 cases reported was the	31. It should so breated from
	C.	Promoted to E-5 1	
	20.7	Promoted to E-4 3	
- 10	e.	Promoted to E-3 6 CATHOLIC FROTE-TANT	
	f.	Medal Awards:	
		Good Conduct 23	
	12.0	1st Award 3 2nd Award 7	
	d.	3rd Award 4	
8.	Pak	4th Award 6 5th Award 3	
	g.	Letters of Commendation.	<i>i</i>
	b.	(1) The following 5 letters of commendation wer	e presented.
	0.	Newspaper in the published 32.	ENCLOSURE (1)
	d.	Fimily grams 1.	

Number of preventive dentistry procedures accomplished 279

MCB-62:6290:hn 1650 Ser: 751 May 1, 1967

Commanding Officer, U. S. Naval Mobile Construction Battalion From: SIXTY-TWO

Builder (Concrete) Third Class Billy Ray LEE, USN, B30 86 31 To:

Construction of 4/12 Marines Cantonment; exceptional performance Subj: of duty during

(1) Copy of CO, 4/12 Marines, 3rd MARDIV (Rain) FMF ltr 6:DCJ:djv of 6 March 1967

- 1. Enclosure (1) describes the attitude and enthusiasm displayed by the men of this Battalion during construction of the 4/12 Marine Headquarters Cantonment, and commends, in particular, your professional competence, leadership, and supervision, as having been major factors in the expeditious accomplishment of the project.
- 2. It gives me great pleasure to note your outstanding performance as set forth in enclosure (1). You may feel a genuine sense of pride in the crew's accomplishment under your supervision of construction in direct combat support to elements of the 3rd Marine Division and other activities in the Phu Bai Combat Base Area. I wish to add to the comments in enclosure (1) the Navy's traditional "WELL DONE".
- 3. A copy of this letter and enclosure hereto will be made an official part of your Naval Service Jacket.

W.J. RICHESON

Copy to: BUPERS (w/encl (1)) SERVICE JACKET (w/encl (1))

MCB-62:6210:ry 1650 Ser: 807 May 9, 1967

From: Commanding Officer, U. S. Naval Mobile Construction Battalion

SIXTY-TWO

To: CEW3 Allen T. Davis, Jr., B30 66 41, USN

Subj: Letter of Commendation

- 1. While standing your watch as a member of the U. S. Naval Mobile Construction Battalion SIXTY-TWO Security Element at the MCB SIXTY-TWO Camp in Phu Bai, Vietnam, at 0135 in the morning of 28 April 1967, you observed muzzle flashes from weapons being fired from outside the Phu Bai Combat Base perimeter. Correctly identifying these flashes as enemy mortar fire you immediately alerted the Command Post to the attack. Then, by use of a compass and the flash-bang method of range determination, you obtained an azimuth and approximate range of the enemy weapons positions. It was later determined that your approximation was accurate to a high degree.
- 2. Your prompt report of the action and the accuracy of your information were the initial and primary source of fire control data that enabled friendly artillery to take the Viet Cong positions under counter-battery fire. Your actions undoubtedly were a major contributing factor in reducing the number of rounds fired by the enemy, thereby lessening casualties in the Combat Base to both personnel and equipment, and reflect credit upon yourself, your Battalion and the Naval Service. It gives me great pleasure to extend to you the Navy's traditional "WELL DONE".
- 3. A copy of this letter will be made a permanent part of your service record.

W.J. RICHESON

Copy to: BUPFRS Service Record Service Record

Turns described a gent buller of the first of the state of the stat

friendly intillers in the de Design regisions who counter-buttery

Bur Contact that I was a real for the contact the contact throw the contact through th

MCB-62:6210:ry 1650 Ser: 808 May 9, 1967

From: Commanding Officer, U. S. Naval Mobile Construction Battalion

SIXTY-TWO

To: CN Reginald A. Hodge, 675 77 82, USN

Subj: Letter of Commendation

- 1. While standing your watch as a member of the U. S. Naval Mobile Construction Battalion SIXTY-TWO Security Element at the MCB SIXTY-TWO Camp in Phu Bai, Vietnam, at 0135 on the morning of 28 April 1967, you observed muzzle flashes from weapons being fired from outside the Phu Bai Combat Base perimeter. Correctly identifying these flashes as enemy mortar fire, you immediately alerted the Command Post to the attack, Then, by use of a compass and the flash-bang method of range determination, you obtained an azimuth and approximate range of the enemy weapons positions. It was later determined that your approximation was accurate to a high degree.
- 2. Your prompt report of the action and the accuracy of your information were the initial and primary source of fire control data that enabled friendly artillery to take the Viet Cong positions under counter-battery fire. Your actions undoubtedly were a major contributing factor in reducing the number of rounds fired by the enemy, thereby lessening casualties in the Combat Base to both personnel and equipment, and reflect credit upon yourself, your Battalion and the Naval Service. It gives me great pleasure to extend to you the Navy's traditional "WELL DONE".
- 3. This letter will be made a permanent part of your service record.

W.J. RICHESON

Copy to:
BUPERS
Service Record

MCB-62:6210:ry 1650 Ser: 809 May 9, 1967

From: Commanding Officer, U. S. Naval Mobile Construction Battalion

SIXTY-TWO

To: BUL3 Lawrence E. MILLER, 682 44 22, USN

Subj: Letter of Commendation

- 1. While standing your watch as Tower Sentry at 0135 on the morning of 28 April 1967, you observed enemy mortar rounds impacting in the vicinity of the airfield adjacent to U. S. Naval Mobile Construction Battalion SIXTY-TWO's Camp in the Phu Bai Combat Base, Vietnam. You unhesitatingly sounded the mortar alarm alerting the Camp and adjacent units of the attach. You then ran to the Command Post Bunker to apprise The Command Duty Officer of what you observed, later you returned to your post, to ascertain if the all clear should be sounded.
- 2. Your prompt response and timely effective action in alerting the Camp and adjacent units undoubtedly were instrumental in avoiding any casualties that might have occured, and reflects credit upon yourself, your Battalion and the Naval Service. It gives me great pleasure to extend to you the Navy's traditional "WELL DONE".
- 3. This letter will be made a permanent part of your service record.

W.J. RICHESON

Copy to: BUPERS Service Record

MCB-62:6210:ry 1650 Ser: 810 May 9, 1967

From: Commanding Officer, U. S. Naval Mobile Construction Battalion

SIXTY-TWO

To: CN John K. GILPIN, 788 27 57, USN

Subj: Letter of Commendation

- 1. While standing your watch as Gate Semtry at U. S. Naval Mobile Construction Battalion SIXTY-TWO's Camp in the Phu Bai Combat Base, Vietnam, at 0135 on the morning of 28 April 1967, you observed enemy mortar rounds impacting the adjacent III Marine Division Cantonment. You immediately realized the gravity of the situation and telephoned the Command Post Bunker to alert the Command Duty Officer of the attack and ordered the switch board operator to sound the mortar alarm.
- 2. Your prompt summation of the imminent danger and instant, correct response were instrumental in providing the corroborating information that there was a mortar attack in progress and of its extent. You further remained at your position and telephoned additional information on the attack to the Command Post. Your actions reflect credit upon yourself, your Battalion and the Naval Service. It gives me great pleasure to extend to you the Navy's traditional "WELL DONE".
- 3. A copy of this letter will be made a permanent part of your service  $\operatorname{record}_{\bullet}$

W.J. RICHESON

Copy to: BUPERS Service Record

#### 10. Civic Action

- a. A total of 926 persons (1,769 treatments) received medical care at daily village sick call. Minor surgical operations were performed on two villagers at the Battalion dispensary. Transportation was provided to Alfa-Med for a villager visiting a hospitalized family member. Dental care was rendered to 37 persons in the form of extractions.
- b. Thuy Chau village received 5 rolls of barbed wire and 25 steel posts for fencing in the village headquarters. Cement (USAID 100 bags) was delivered for the repair of one school (50 bags), and for the construction (50 bags) of three bamboo and cement pig pens to house pigs from the III MAF Agricultural Farm in Danang. A rice threshing machine was also demonstrated and future plans for distribution of these machines were made when they become available. Hydrated cement (180 bags) was also delivered to the Catholic Than Phu Orphanage. The Hue Technical School received one (1) engine block, two (2) transmissions, two (2) wash machines and used oil filters. Students (40) from the school were also picked up by Battalion vehicles and given a one day tour of Camp Campbell and activities of the various companies.
- c. The Chaplain made bi-weekly visits to the Than Phu Orphanage for English instruction.

MATER HANDI	RIAL .	CONS	rauctio	ON	AUTO	MOTIVE		· 图 3	
AUGMENT	P25A	SUPP FUNC COMP	AUGMENT	P25A	AUGMENT	P25A	31.54	TYPE ON EQUIPMENT	
1	6	16	60	114	10	139		NUMBER ASS I GIVED	
0	0	0	0	0	0	0	TCTAVITATO	NUMBER BORROWED OR	EQUIPMENT STATUS
1	6	16	60	114	10	139	TIME	TOTAL ON	TATUS
0	0	0	8	2	0	0	ADDED TO D/L	DURING REPORTING	
0.	0	0	N	2	0	W	OFF D/L	DURING REPORTING PERIOD	UNIT**** MCB 62
0	0	N	00	13	0	10	END OF PERIOD		2 25 APR to 25 MAY 67

Supply Dept.	Blue Jackets Man. Ch. 1, 2, & 3	1 Hr.	4
Supply Dept.	Blue Jackets Man. Ch. 4, 5, & 6	1 Hr.	12
Supply Dept.	Blue Jackets Man. Ch. 7 & 8	l Hr.	12
Supply Dept.	Blue Jackets Man. Ch. 9,10, & 11	1 Hr.	12
Supply Dept.	Review of Officers Mess Organiz.	1 Hr.	5
Supply Depte	Review of Sanitation in the	•	
	Wardroom and Galley	1 Hr.	. 5
Supply Dept.	Review of the Operation and Care		
	of Galley Equipment	l Hr.	5
Supply Dept,	Review of Mess Management	1 Hr.	ź

# 2. Correspondence Courses and Extension Courses:

		Enrolled	Completed
a.	Officers Courses	2	0
b,	Enlisted Courses	43	67
c.	USAFI	5	0
3.	Examinations Adminis	stered:	
$a_{\rm e}$	USAFI/GED ETC.	11	

b. Advancement in Rate 21

E-3 21

E-4 0

E-5 0

E-6 0

E-7 0

## LABOR DISTRIBUTION REPORT

UNIT NMCB 62 PERIOD ENDING 28 May 19 67

WORK DAYS THIS PERIOD-31		MANDAYS		PERCENT TOTAL UNIT LABOR
NMCB AVG ON BOARD PERSONNEL AT EMPLOYMENT SITE 782	UNIT	OTHER	TOTAL	AVAILABLE
DIRECT LABOR	OIVII	Ollitat	10 1111	TIVITEDITE TO THE TOTAL TO THE TOTAL TOTAL TOTAL TOTAL TOTAL TO THE TOTAL TOTA
TOTAL CI DIRECT LABOR				
TOTAL FILL-IN DIRECT				
TOTAL DIRECT LABOR	12845		12845	48.6%
INDIRECT LABOR XOL CONST EQUIP MAINT	2665		2665	
REPAIR AND RECORDS XO2 OPERATIONS AND ENGINEERING	822		822	
XO3 PROJECT SUPERVISION XO4 PROJECT EXPEDITING (SHOP PLANNER)	918 73		918 73	
XO5 LOCATION MOVING XO6 PROJECT MATERIAL SUPPORT	23 500		23 500	
XO7 TOOL AND SPARE PARTS ISSUE	372		372	
XO8 OTHER	198		198	
TOTAL INDIRECT LABOR	5571		5571	21.1%
MILITARY OPERATIONS AND READINESS MOL MILITARY OPERATIONS MO2 MILITARY SECURITY MO3 EMBARKATION MO4 UNIT MOVEMENT MO5 MOBILITY PREPARATION	1848		1848	
MO6 CONTINGENCY MATERIAL READINESS MO7 MILITARY ADMINISTRATIVE	231		231	
FUNCTIONS MO8 MOBILITY & DEFENSE EXERCISES MO9 OTHER				
TOTAL MILITARY OPS AND READ	2079		2079	7.8%

		MANDAYS		PERCENT. TOTAL UNIT LABOR
	UNIT	OTHER	TOTAL	AVAILABLE
DISASTER RECOVERY OPERATIONS DO1 DISASTER RECOVERY OPS DO2 DISASTER RECOVERY EXERCISES			and the second s	
TOTAL DISASTER RECOVERY OPS				
TRAINING TO1 TECHNICAL TRAINING TO2 MILITARY TRAINING TO3 DISASTER RECOVERY TRAINING TO4 LEADERSHIP TRAINING	47		47 3	
TO5 SAFETY TRAINING TO6 TRAINING ADMIN	23		23	
TOTAL TRAINING LABOR	73		73	0.3%
TOTAL PRODUCTIVE LABOR	20568		20568	77.8%
OVERHEAD LABOR YO1 ADMIN & PERSONNEL YO2 MEDICAL AND DENTAL DEPTS YO3 SHIPS SERVICE & SPECIAL SERVICES YO4 SUPPLY & DISBURSING YO5 COMMISSARY YO6 CAMP UPKEEP & REPAIR YO7 SECURITY YO8 LEAVE & LIBERTY YO9 SICKCALL, DENTAL & HOSPITALATION Y10 PERSONAL AFFAIRS Y11 LOST TIME Y12 TAD NOT FOR UNIT Y13 OTHER	721 341 174 508 1647 689 477 944 222 41 37 35 5		721 341 174 508 1647 689 477 944 222 41 37 35 5	22.1%
TOTAL OVERHEAD LABOR	5841		5841	22.1%
TOTAL LABOR AVAILABLE	26409		26409	100%

## INDEX OF CONSTRUCTION SUMMARIES

PAGE	PROJECT NO.	DESCRIPTION
7	6DFI43201	FLSG/A REFRIGERATION
1 2	6DSA44201	FLSG/A COVERED STORAGE
2	6DSA21403	FLSG/A MAINTENANCE SHOPS
ر ا.	6DSA44204	FLSG/A CANTONMENT
3 4 5 6	6DSA45114	FLSG/A OPEN STORAGE
2	6DSA85115	FLSG/A ROADS
7	6DSA87116	FLSG/A DRAINAGE
7 8		
	6DSA45417	FISC/A OPTICAL SHOP
9	6DSA55018	FLSG/A DISPENSARY
10	6DSA74024A	FLSG/A COMMUNITY FACILITIES
11	6DSA87227A	FLSG/A COMMUNITY CENTER FENCE
12	6DSA87222A	FLSG/A FENCING
13	6DMA73001A	FLSG/A BAKERY
14	6DPA73001A	FLSG/A FIRE STATION
15	6DSG21520A	FLSG/A WEAPONS/COMMUNITY MAINTENANCE
16	MCB 62-186E	FLSG/A CHAPEL
1.7	6DFI43202	FLSG/A REFRIGERATION SHED
18	6DJA <b>72501</b>	OLD FLSU-95 STRONGBACK CONVERSIONS
19	6CMA <b>72</b> 55 <b>1A</b>	FLSG/A CANTONMENT (2)
20	6DEA21001A	3RD MARDIV, LARF BUILDINGS (SHOPS)
21	6DDA21002A	3RD MARDIV LRF BUILDINGS
22	6DDA44201	3RD MARDIV 5RF BUILDINGS
23	6AFA44204A	3RD MARDIV 18RF BUILDINGS
24	6DNA74001A	3RD MARDIV DENTAL CLINIC
25	6DQA72564	3RD MARDIV LTH INCREMENT
26	6DQA72566	3RD MARDIV 4TH INCREMENT
27	6ANA 72528A	
-1	6APA72558A	3RD MARDIV 6TH INCREMENT
	MCB62-106E	Jan Indiana I Carl Militaria
28	6AYA84009A	WEILS, 3RD MARDIV
29	6DLA72001	R & R CANTONMENT, PHU BAI
30	6DBA85104A	3RD MARDIV 7 CONCRETE SLABS
31	6DEA61902A	3RD MARDIV DISPENSARY
32	MCB 62-149E	FINAL GRADING FOR 1st, 2nd, 3rd, &4th CANTONMENTS
33	MCB 62-187E	3RD MARDIV GARBAGE HOUSE, 3RD INCREMENT
34	6ADA21/11A	3RD MARDIV 4RF BUILDINGS (SHOPS)
35	6LZZ00045D	3rd MARDIV MORTAR OBSERVATION TOWERS
	6DJA72502	MAG 16 - 20 STRONGBACK CONVERSIONS
36 37	The state of the s	25 STRONGBACKS FOR MAG 16
37	MCB 62-154E	
38	6CEA21912A	1ST MAW 1RF BUILDING
39	MCB 62-248E	ACCESS ROADS & FUEL BERMS, 1ST MAW
40	MCB 62-221E	MAG 16 3 SATS HANGARS
Lil.	7XXX0004E	WELL FOR MAG 16
42	6DBX11301A	VMO PARKING APRON
	6LZZ00025	T-17 MAT EXTENSION
43	FSI 7-01	HUE INTERROGATION CENTER
7171	FSI 30 CP-A	POWER POLE CASTING YARD

P.	Δ	G.	E

45 46 47 48 49 55 55 55 55 55 55 55 56 66 66 66 67 66 70 71	FSI 80-A FSI-92A FSI 102A FSI 132005A FSI 132007A FSI 132008A 6DBA85102 6LZZ00050D 6DUE85103A 6DUE15305A MCB 7-21 MCB 62-01 6DSAL5106 6DDA21004A 6DTA72501A 6DTB11302A 6DTA80103A MCB 62-283E 6DSA81209 6DCA84101 7XXX05229E 6DSA55019 7DVD131C0 6P0A21 MCB 62-264E MCB 7-04 MCB 62-185E	811TH ORDNANCE TRACK REPAIR TEAM FSI GRAVES REGISTRATION PLT. DIV Q.M. REPAIR DETACHMENT, HUE 227TH REG FORCE RIFLE CO. 239TH REG FORCE RIFLE CO. 217TH REG FORCE RIFLE CO. ROAD MAINTENANCE, PHU BAI ROUTE 1 IMPROVEMENT ROUTE 551 IMPROVEMENT HUE RAMP EMERGENCY REPAIRS COLCO ROAD SEABEE CANTONMENT SEABEE QUARRY SEABEE BATCH PLANT 131ST AVIATION CANTONMENT 131ST AVIATION GENERATOR SHED 131ST AVIATION WELL POWER DISTRIBUTION SYSTEM WATER SUPPLY, PHU BAI REHAB PHU BAI AIRFIELD A-MED 2ND ADDITION DIAL CENTRAL OFFICE LOG PERIODIC ANTENNA-8TH RRU PA & E CONSTRUCTION ASSISTANCE DONG DA SOG HUE RAMP (1) STRONGBACK

# FISCAL SUMMARY OF CONSTRUCTION OPERATIONS

UNIT NMCB SIXTY-TWO	PERIOD	ENDING 25 May 1967
	DURING REPORTING PERIOD	DEPLOYMENT TO DATE
PROJECT SUPPORT COSTS (BP 40 MILCON)	0	\$2,630,19
PROJECT EQUIPMENT SUPPORT COSTS (BP 68 AUTOMOTIVE)	\$33,004.79	\$210,641.52
PROJECT MATERIAL IN PLACE	\$664,688.45	\$1,236,298.25

#### PROGRESS PHOTOGRAPHS

#### CAPTION PAGE FOR 8" X 10" BLACK AND WHITE PHOTOGRAPHS

- 1. Aerial view of 3RD Marine Division Area at Phu Bai. Left foreground 4/12 Artillery; Right foreground 155 Guns both recently completed by MCB 62. Butlers in right center recently completed or under construction.
- 2. VMO soil-cement parking apron and T-17 membrane/M8Al parking area near completion, Project Nos. 6DBX11301A & 6LZZ0025B.
- 3. Water Treatment Plant for the Phu Bai Water System under construction. Project No. 6DCA84102A
- 4. Almost 1/3 of the brickwork (283,503 bricks) for the Hue Interrogation Center has been completed. Project No. FSI 7-01
- 5. The Seven Mortar Towers were partially constructed on the ground by Delta Company Builders, then set in place with a mobile crane. Project No. 6LZZCO45D
- 6. Bravo Company's CEs then helped set the platform and remaining cross-bracing. The completed towers are used to spot enemy mortar or rocket flash and direct the return of friendly fires. Project No. 6LZZOO45D
- 7. Completed 3rd Motor Transport Battalion Galley (top) and 3rd Medical Battalion Galley (bottom). Project No. MCB62-106E
- 8. Concrete post and barbed wire fence for the Hue Ramp. Project No. 6DUE1530
- 9. Exterior work for the Dial Central Building is now complete. Project No. 6DVD13100
- 10. Construction of "B" Road in the 3rd Marine Division Area. Project No. 6DBA85102
- 11. Three of the strongbacks for the 131st Aviation Company are made into an L-shaped enlisted club. Project No. 6DTA72501A
- 12. Laying the T-17 membrane and M8Al matting. The locking pins are being driven with a jackhammer. Project No. 6LZZOO025B
- 13. Commander W.J. RICHESON, Commanding Officer MCB 62, welcomes Captain C.G. MILLER to Camp Campbell.
- 14. Letters of commendation were presented to J.K. GILPIN, CN, of Delta Company (left) and L.E. MILLER, BUL3 of Charlie Company for their quick action during the 4-28-67 mortar attack on the Phu Bai Combat Base.
- 15. Letters of commendation were presented to A.T. DAVIS Jr., CEW3, of Bravo Company, and R.A. HODGE, CN, of Delta Company for their quick action during the 4-28-67 mortar attack on the Phu Bai Combat Base. (top) Good conduct awards were presented to: Left to right CRASCO, J.F. CS1, HARKINS, L. Jr. SH1, TRONBLEY, W.D. SK1, COULOMBE, L.J. Jr. GMG3, WHITAKER, J.L. EOH2, DUGGER, H.D. UTCS, CRAHAM, P.B. SWC, GALEY, T.A. CEC, MANNING, R.B. CEC, ACHESON, M.W. Jr. BUC, KESSINGER, N.R. BU1, STONE, F.A. BU1.
- 16. Time for another (ouch!) Gamma Globulin shot.

## Hue Interrogation Center (FSI 7-01)

- 1. "Digging footings. Laterite pad which was once soup is now rock.
- 2. Digging footings
- 3. Loading concrete into borrow to place footings.
- 4. Placing concrete footings.
- 5. Forming Columns.

#### Miscellaneous

- 6. Erecting a SATS hangar for use by MAG-16 Helicopter Squadrons on the VMO Parking Apron. (MCB 62-221E)
- 7. Erecting 25 strongback huts on the VMO Parking Apron, to be used as squadron offices and living quarters. (MCB 62-154E)
- 8. Placing concrete steps for Dial Central using a homemade concrete bucket made from a 55 gallon drum. (7DVD13100)

## 7 Mortar Observation Towers (6LZZ00045D)

- 9. Setting one of the two prefabricated sides of the 50' mortar observation tower.
- 10. After one side is up, braces are scabbed on to allow it to stand free.
- 11. One side is up and the other is held by a crane while Delta Company Seabees prepare to scab the two sides together.
- 12. Two sides are now in place and the cross-bracing of the two together proceeds.
- 13. The prefabricated tower platform being raised to place.

## Various Butler Bldg, Projects

- 14. An MRS Scraper is assisted by an Eimco tractor in cutting a hill to provide fill for Butler Buildings in the 3rd Marine Division, area, Phu Bai.
- 15. Charlie Company men set forms for a Butler Building footing in the FLSG/A cantonment.
- 16. Sag rods are put in place on one of the 3rd Marine Division Butler warehouses.

- 17. Structural Steel goes up on a 3rd Marine Division Butler Building.
- 18. The structural frame nears completion on one of a series of Butler Building warehouses in the 3rd Marine Division.
- 19. Roof sheeting goes in place on one of the 3rd Marine Division Butler Buildings.

#### Miscellaneous

- 20. A clamshell digs out a culvert under 'B' Road leading into the 3rd Marine Division, 4th cantonment, from Route 1 prior to resetting the culvert. (6DQA72504)
- 21. Forms being constructed for concrete feace posts to be set at Hue LCU Ramp. (6DUE15305A)
- 22. Transit mixers line up at MCB-62's Batch Plant. (6DDA21004A)
- 23 Vapor barrier being set in place prior to placing concrete deck slab in Dial Central Building. (7DVD13100)
- 24. A Seabee lends a helping hand in repairing a damaged LCU at the Hue Ramp.

#### CBPAC SLIDES

#### Hue Interrogation Center (FSI 7-01)

- 1. "Digging" footings. Laterite pad which was once soup is now rock.
- 2. Digging Footings
- 3. Loading concret into barrow to place footings
- 4. Placing reinforcing steel for slab.
- 5. Forming Columns.
- 6. Washing aggregate before using it in concrete.
- 7. Placing footings while ARVN soldiers watch.

## VMO T-17 Extension (6LZZ00025B)

- 8. Spreading T-17 fabric membrane on laterite sub-base.
- 9. Applying glue at fabric seam.
- 10. Lapping the edges of the T-17 membrane over the glue.
- 11. Placing M8Al matting over the T-17 membrane.
- 12. Driving the locking pins in the M8Al planks home.

## 7 Mortar Observation Towers (6LZZ00045D)

- 13. Setting one of the two prefabricated sides of the 50' mortar observation tower.
- 14. After one side is up, braces are scabbed on to allow it to stand free.
- 15. One side is up; the other is held by a crane while Delta Company Seabees prepare to scab the two sides together.
- 16. Two sides are now in place and the cross-bracing of the two together proceeds.
- 17. The prefabricated tower platform being raised to place.

## Various Butler Bldg. Projects

- 18. An MRS Scraper is assisted by an Eimco tractor in cutting a hill to provide fill for Butler Buildings in the 3rd Marine Division area, PHU BAI
- 19. Charlie Company men set forms for a Butler Building footing in the FLSG/A Cantonment.

- 20. Structural Steel goes up on a 3rd Marine Division Building.
- 21. The structural frame nears completion on one of a series of Butler Building Warehouses in the 3rd Marine Division area.
- 22. Roof sheeting goes in place on one of the 3rd Marine Division Butler Buildings.

#### Miscellaneous

- 23. Transit mixers line up at MCB-62's Batch Plant. (6DDA2100lA)
- 24. A clamshell digs out culvert under 'B' road leading into the 3rd Marine Division, 4th Cantonment, from Route 1 prior to resetting culvert. (6DQA72564)
- 25. Charlie Company erects a 250-man galley for the 3rd Motor Transport Battalion. (MCB 62-106E)
- 26. A Seabee lends a helping hand in repairing a damaged LCU at the Hue Ramp.



U. S. Haval Mobile Construction Battalion Sixty-Two FPO How York, New York 09501

OFFICIAL U.S. HAVY PHOTO HOT FOR PUBLICATION UTLESS OFFICIALLY RELFASED

CB-62-1246-5-67 5-16-67

PHU BAI, VINTUAL

Aerial view of 3rd Marine Division Area at Phu Bai.
Left foreground - 4/12 Artillery; right foreground 155 Guns - both recently completed by MCB-62.
Butlero in right center, recently completed or under
construction.




# U. S. Maval Hobile Construction Battalion Sixty-Two FPO New York, New York 09501

OFFICIAL U.S. HAVY PHOTO NOT FOR PUBLICATION UNLESS OFFICIALLY RELEAS D

HCB-62-1259-5-67 **5-1**6-67 6DBX11301A 6LZZO025B PHU BAI, VIETNAII

WTO soil-cement parking apron and T-17 membrane/ H8Al parking area near completion.

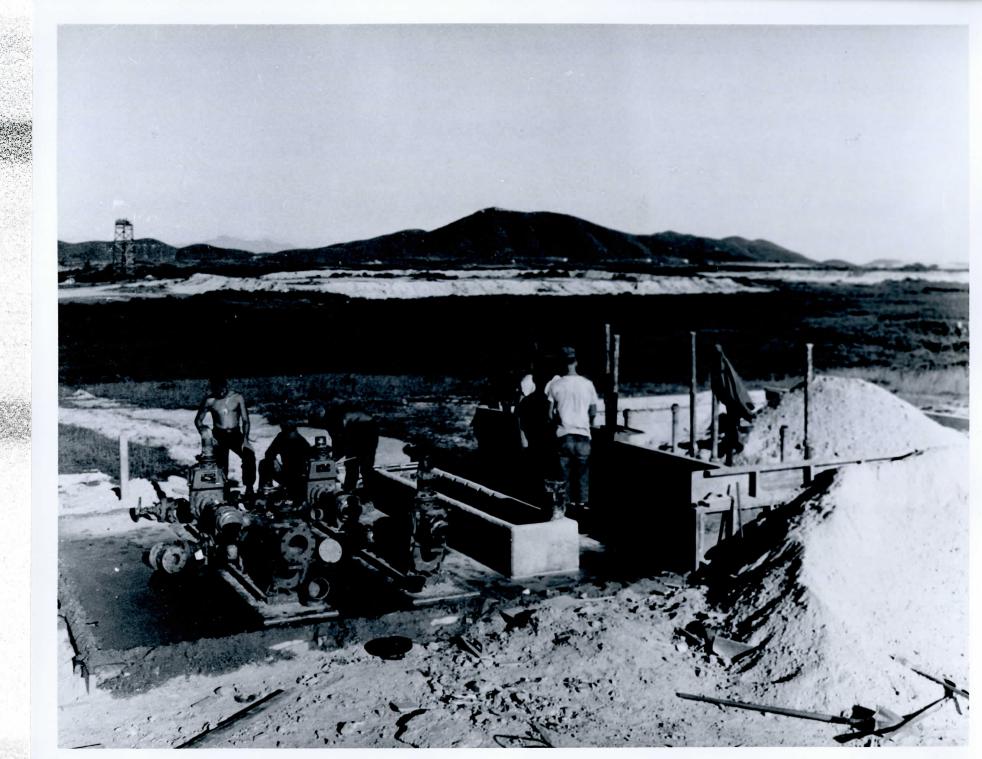

# U. S. Maval Hobile Construction Battalion Sixty-Two FPO New York, New York 09501

OFFICIAL U.S. MAVY PHOTO NOT FOR PUBLICATION UNLESS OFFICIALLY REMASED

16B-62-1316-5-67 5-26-67 6DCA6L101 PHU BAI, VIETM**A**M

Water Treatment Plant for the Phu Bai Water System under construction.





# U. S. Naval Mobile Construction Battalion Sixty-Two FPO Hew York, New York 09501

OF ICIAL U.S. MAVY PHOTO NOT FOR PUBLICATION UNLESS OFFICIALLY RELEASED

(top) HCB-62-1308-5-67 (bot) HCB-62-1307-5-67 5-25-67

FSI 7-01 HUE, VICTNAN

Almost 1/3 of the brickwork (283,503 bricks) for the Mue Interrogation Center has been completed.






U. S. Haval Mobile Construction Dattalion Sixty-Two FPO Hew MCRK, How York 09501

OFFICIAL U.S. MAY PHOTO FOR FUBLICATION UNLESS OF TOTAL Y RITHAS ()

(top) MCB-62-1181-5-67 (bot) MCB-62-1170-5-67 5-5-67

61ZZ0045D PHU BAI VIETMAN

The Seven Mortor Towers were partially constructed on the ground by Delta Company Buildors, then set in older mith a mobile crane.

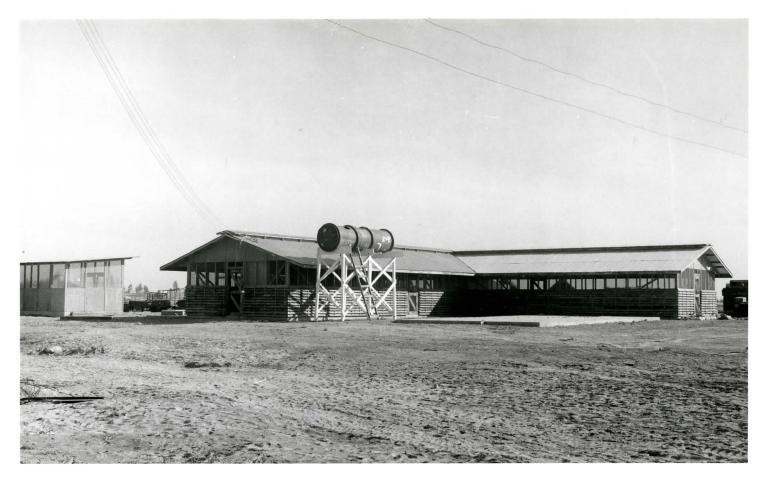



# U. S. Naval Mobile Construction Battalion Sixty-Two FPO Hew York, New York 09501

OFFICIAL U.S. HAVY PHOTO HOT FOR PUBLICATION UNLESS OFFICIALLY RELEASED

(top) 103-62-1294-5-67

HCB-62-106E

5-20-67 (bot) MCB-62-1218-5-67 5-15-67

PHU BAI, VINNAM

Completed 3rd Motor Transport Battalion Calley (top) and 3rd Medical Battalion Calley (bottom).




## U. S. Maval Mobile Construction Sattalion Sixty-Two FPO Mew York, Mew York 09501

OF ICEAL U.S. MAVY PHOTO MOT FOR PUBLICATE H UPLESS OFFICIALLY RELEASED

110B-62-1299-5-67 5-25-67 6DUE15305A HUE, VIETEAN

Concrete post and barbed wire fence for the Rue Ramp.

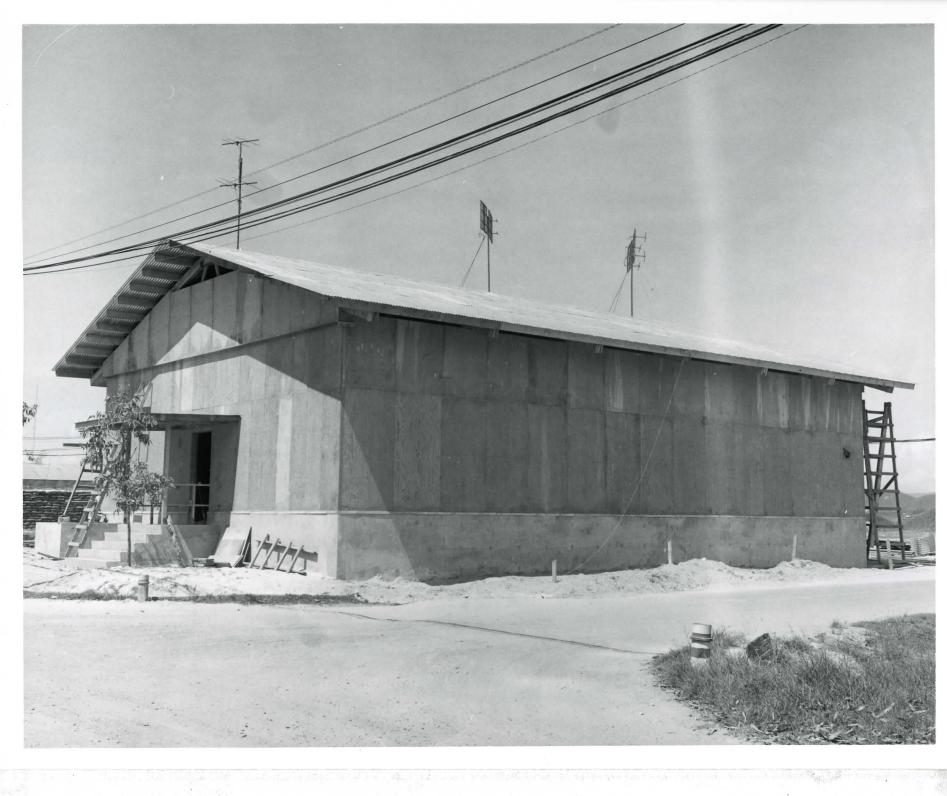

U. S. Maval Mobile Construction Battalion Sixty-Two FPO Hew York, Mew York 09501

OFFICIAL U.S. MAVY PYOTO MOT FOR TUBLICATION UNLESS OWNEDIALLY EMPLASED

HCB-62-1214-5-67 5-15-67

6DVD13100 PHU BAI, VITTHAN

Exterior work for the Dial Central Building is now complete.



## U. S. Haval Mobile Construction Battalion Sixty-Two FPO Hew York, New York 09501

OFFICIAL U.S. HAVY PHOPO HOT FOR PUBLICATION UNLESS OFFICIALLY RELEASED

F03-62-1297-5-67 5-20-67

6DBA85102 PINI BAI, VIETHAN

CONSTRUCTION OF "B" ROAD IN THE 3rd MARINE DIVISION



U. S. Maval Mobile Construction Battalion Sixty-Two FPO New York, Mew York 09501

OFFICIAL U.S. MAYY PECTO NOT FOR PUBLICATION UNLESS OFFICIALLY ROLLAND


1103-62-1220-5-67 **5-1**5-67 6DTA72501A PHU BAI, VIETNAM

3 of the strongbacks for the 131st Aviation Company are made into an L-shaped enlisted club.







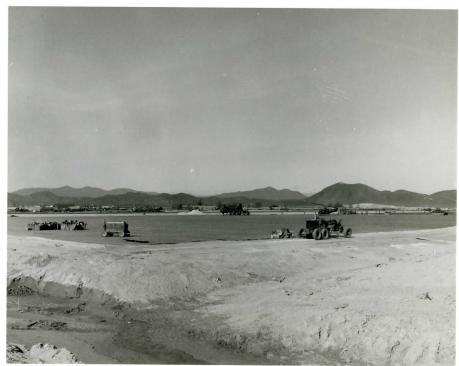

U. S. Havel Hobile Construction Battalion Sixty-Two FPO New York, New York 09501

OFFICIAL U.S. MAVY PHOTO NOT FOR PUBLICATION UNLESS OFFICIALLY RELEASED

(top-L) MCB-62-1163-5-67 (top-R) MCB-62-1162-5-67 (bot-L) MCB-62-1295-5-67 (bot-R) MCB-62-1293-5-67 (bot-R) MCB-62-1293-5-67 6LZZOCOCC PHU BAI, VIETNAM

Laying the Tol7 membrane and N8Al matting. The locking pins are being driven with a jackhammer.



U. S. Maval Mobile Construction Battalion Sixty-Two FPO Hew York, New York 09501


OFFICIAL U.S. MAVY PHOTO OF FOR PUBLICATION ULLESS OFFICIALLY RELEASED

NCB-62-1223-5-67 5-15-67

PHU BAI, VIETNAM

CDR. W. Richeson, Commanding Officer of MCB-62, welcomes CAPT C. G. Miller to Camp Campbell.



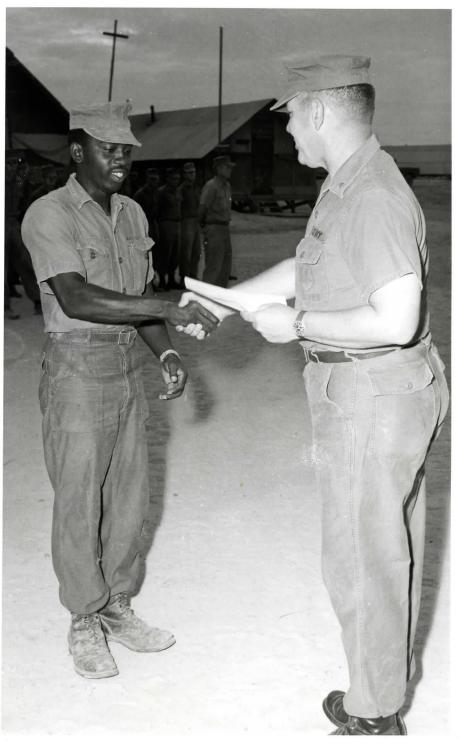


U. S. Mavel Hobile Construction Battalion Sixty-Two FPO Hew York, Hew York 09501

OFTICIAL U.S. HAVY PROTO HOT FOR PUBLICATION UNLESS OFFICIALLY RULEASED

(left) MCB-62-1227-5-67 (right) MEB-62-1226-5-67 PMU BAI, VIETMAN

Letters of commendation were presented to J.K. Gilpin, of Delta Com any(left) and L.T. Miller, BUL3 of Charlie Company for their quick action during the h/28/67 mortar attack on the Phu Bai Combat Base.

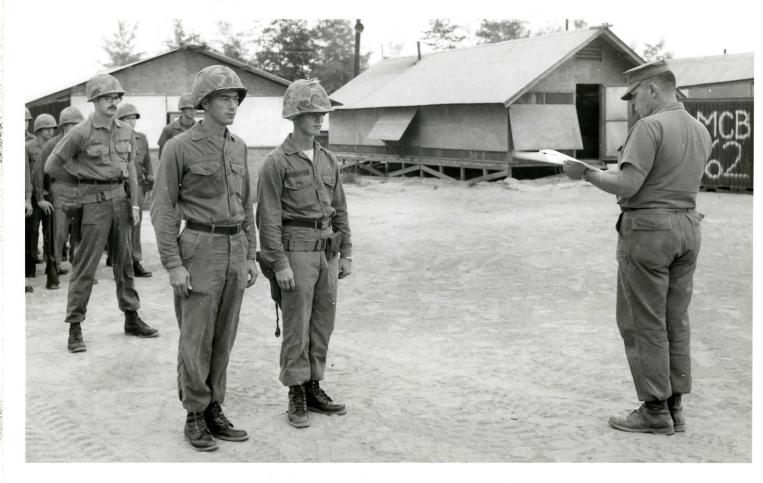




## U. S. Maval Mobile Construction Battalion Sixty-ino

OF ICIAL U.S. MAVY PHOTO MOT FOR MUBLICATION MILESS OFFICIALLY ROLLASED

(top) HCB-62-1235-5-67 5-15-67 (bot) HCB-62-1283-5-67 PHU BAI, VINTNAM 5-21-67

Letters of commendation were presented to A.T. Davis Jr, Chi-3, of Bravo Company, and R.A. Hodge, CN, of Delta Company for their quick action during the 4-26-67 Mortor attack on the Phu Bai Combat Base. (top)

Good Conduct Awards were presented to:
Crasco, J.F., CS-1; Markins, L., SH-1; Trombley, W.D.,
SK-1; Goulonbe, L.T., G.G-3; Whitaker, J.L., EOH-2;
Dugger, H.D., UTCS; Graham, P.B., SWC; Galey, T.A.,
CEC; Manning, R.B., CEC; Acheson, M.W., BUC;
Kessinger, N.1., BU-1; and Stone, F.A., BU-1.

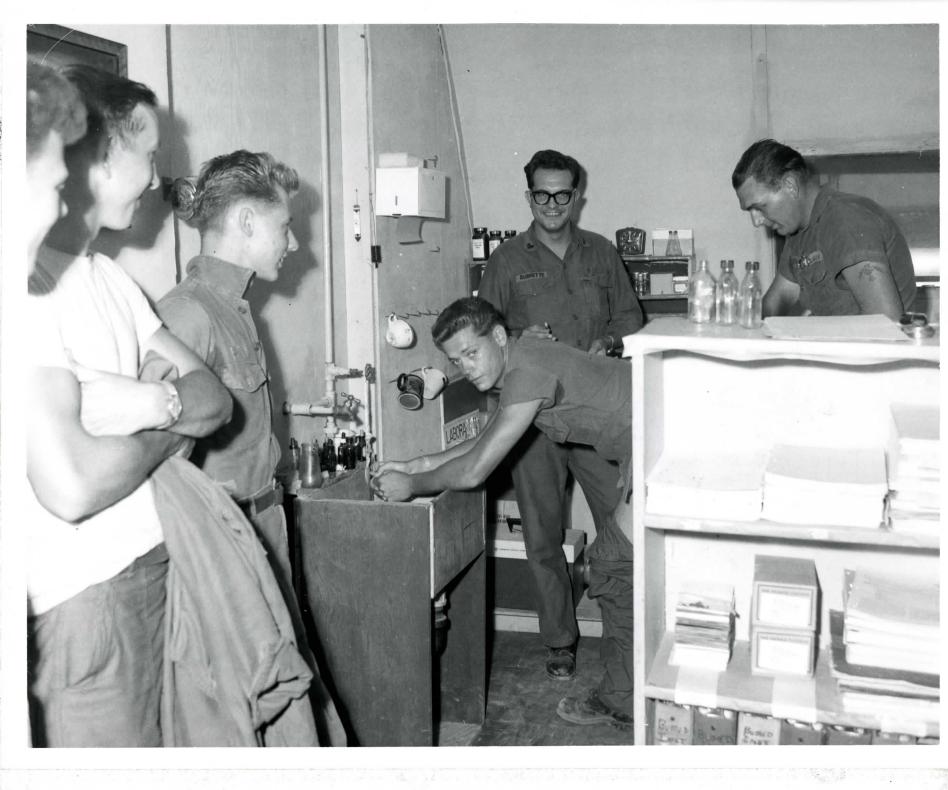

U. S. Naval Mobile Construction B attalion Sixty-Two FPO New York, Hew York 09501

OFFICIAL U.S. FA/Y PROTO NOT FOR PUBLICATION UNLESS OFFICIALLY RELEASED

10B-62-1292-5-67 5-22-67

PHU BAI, VIETNAM

Time for another (OUCH!) Gamma Globulin shot.
