

U.S. NAVAL MOBILE CONSTRUCTION BATTALION SIXTY-TWO
Care of Fleet Post Office
New York 09501

12 *SW*
MCB-62:CP0:mdb
5213
Ser 1124
1 July 1967

From: Commanding Officer, U. S. Naval Mobile Construction Battalion
SIXTY-TWO, FPO New York 09501
To: Commander, Naval Construction Battalions, U. S. Pacific Fleet,
FPO San Francisco 96610

Subj: Operations Report for Period Ending 25 June 1967; submission of

Ref: (a) COMCBPAC INST 5213.1C
(b) COMCBPAC OPORD 24-66

- Encl: ✓ (1) Administrative Summary
✓ (2) Equipment Status Report
✓ (3) Training Report
✓ (4) Labor Distribution Report
✓ (5) Construction Item Summary
✓ (6) Progress & Performance Chart
✓ (7) Fiscal Summary
✓ (8) Progress Photographs (Black and White)
✓ (9) Color Slides (*not included*)

1. In accordance with reference (a), MCB SIXTY-TWO's Operations Report for the period 26 May to 25 June 1967 is forwarded herewith.

2. Employment Status. In accordance with reference (b), U. S. Naval Mobile Construction Battalion SIXTY-TWO is deployed to Hue/Phu Bai. The primary mission of the Battalion is construction in support of the 30th Naval Construction Regiment. The following unit is detached.

a. Seabee Team 6201: Deployed to CBC, Gulfport for training.

3. Unit Movements. None

4. Significant Events.

a. During this period the following major projects were completed:

6DSA21403 - FLSG/A Maintenance Shops
6DQA72564 - 3RD MARDIV-4th Increment Cantonment
6DQA72566 - 3RD MARDIV-5th Increment Cantonment
6DSA74024A - FLSG/A Community Facilities

5. Major Problems. None

6. Significant Events Planned.

a. On 2 July, MCB-62 will celebrate its first birthday.

b. From 29 June through 1 July, MCB-62 will participate in the "Hue Olympics," a United States-Vietnamese Armed Forces athletic competition.

c. In early July, MCB-62's advance party will depart Phu Bai for Gulfport and MCB-121's advance party will arrive.


W.J. RICHESON

Copy to: (With enclosures except as indicated)

NAVFACENGCOMD (CODE 50) (2)
CINCPACFLT (1)
COMSERVPAC (1)
COMSERLANT (1)
COMCBLANT (2) (With encl. (9))
COM3ONCB (1) (With encl. (9))
2ONCR (2)
3ONCR (1)
CO, CBCEN, PORHUE (2)
CO, NAVSCOLCONST (1)
CO, NCEL (1)
Dir of NAVAL HISTORY (1)
CG, FMFPAC (1)
CG, III MAF (2)
ALL NMCB's (1 each) (less encl 8)
CO NMCB One Hundred Twenty One (1)
CG, 3RD MARDIV (1)

ADMINISTRATIVE SUMMARY

UNIT NMCB SIXTY-TWO

ADMINISTRATIVE SUMMARY FOR 26 MAY 67 TO 25 JUNE 67.

1. PERSONNEL SUMMARY AS OF 25 JUNE 1967.

	ON BOARD AT DEPLOY- MENT SITE	ATTACHED BUT NOT AT DEPLOY- MENT SITE	TOTAL PERSONNEL ASSIGNED	CHANGES DURING PERIOD	
				RECEIPTS	TRANSFERS
E-9	1	0	1	0	0
E-8	5	0	5	0	0
E-7	34	5	39	2	0
E-6	65	7	72	0	3
E-5	113	27	140	0	4
E-4	280	3	283	0	6
NON-RATED	258	0	258	1	6
TOTAL	756	42	798	3	19
OFFICERS	22	1	23	0	0

Breakdown of personnel attached but not at deployment site.

	DETACHMENT/ DETAIL	SEABEE TEAMS	REAR ECHELON	ADV/DEL PARTY	SCHOOLS	HOSP	BRIG	LEAVE
OFFICER	0	1	0	0	0	0	0	0
ENLISTED	0	12	29	0	0	0	0	4

2. Reenlistments.

- Separations eligible for reenlistment 9. Career 0 Non-career 9
- Reenlistments 1. Career 1 Non-career 0.
- Not recommended for reenlistment 1. Career 0. Non-career 1.
- Personnel receiving separation interviews 100.

3. Safety.

a. Monthly accident summary

	<u>ON DUTY</u>	<u>OFF DUTY</u>	<u>MANDAYS LOST</u>	<u>\$ DAMAGE</u>
FIRST AID	8	2	N/A	N/A
LOST TIME	0	0	14 (carried over)	N/A
VEHICLE	2	0	0	\$300.00

b. Total number of assigned automotive vehicles 137.
Miles driven 108,213.

c. Stand-up safety meetings 36.

4. Discipline.

Number of cases heard at Captain's Mast 14; awarded NJP 13;
Awarded Court-Martial 1.

5. Morale.

a. Overall morale remains excellent. Major repairs have been accomplished on the enlisted club and the MCB-62 all-star Basketball Team remains undefeated, having won eight games from any command desiring a game from the Phu Bai and Gia Le Combat Bases, and Hue.

b. Berthing provided by NMCB-62: condition good.

c. Messing is outstanding. Food preparation, quality and quantity remains outstanding though facilities are still barely satisfactory.

6. Medical/Dental.

a. Total patients treated at sick call 567.

b. Number hospitalized 0.

c. On sick list at end of period 0.

d. Dental patients treated 437.

e. Total dental procedures 1336.

f. Number of personnel in each dental classification:

Class 1 - 344

Class 2 - 349

Class 3 - 58

Class 4 - 22

Class 5 - 0

g. Number of preventive dentistry procedures accomplished 373.

h. Number of new VD cases 8. Total number 35.

i. Total prescriptions filled 122.

7. Chaplain Activities.

	CATHOLIC	PROTESTANT
a. Number of services	4	8

b. Average attendance	35	30
-----------------------	----	----

c. Religious training classes 9.

d. Red Cross 5.

8. Public Relations.

a. FHTNC releases 5.

b. Other media releases 3.

c. Newspaper issues published 1.

d. Family Grams 1.

9. Awards & Promotions.

a. Promoted to E-3 6.

b. Promoted to O-3 1.

c. Medal Awards None.

10. Civic Action.

a. A total of 1,218 persons received medical-dental care at daily village sick call. There were 1,882 medical and 260 dental procedures rendered. One small child was brought to the Battalion Dispensary for incision and drainage of an abscess.

b. The Bai Dao Orphanage in Hue received three bags of sugar, one carton of cooking oil and five pounds of dried milk and soups. The Redemptorist Church in Hue received one hundred and fifty bags of cement. The Phu Luong Orphanage and Diem Tu Refugee Village received twenty five bags of cement and two truck loads of wood respectively.

c. Three pig pens were completed by the villagers and met the agricultural specifications set by the III MarDiv advisor in the Thuy Chau village. Yorkshire pigs will be delivered to those three families as soon as they arrive from Danang.

d. Periodic visits were made with the village chief to check the progress of the pig project and other future projects. The Chaplain made several visits to the Than Phu Catholic Orphanage and held English language instruction.

EQUIPMENT STATUS							UNIT MCB-62	25 MAY 66
							REPORT FOR	25 June 66
TYPE OF EQUIPMENT	NUMBER ASSIGNED	NUMBER BORROWED OR RENTED	TOTAL ON HAND	DURING REPORTING PERIOD		TOTAL NUMBER DEADLINED END OF PERIOD		
				ADDED TO D/L	OFF D/L			
AUTOMOTIVE	P25A	0	137	0	2	8		
	AUGMENT	0	13	0	0	0		
CONSTRUCTION	P25A	0	113	4	3	14		
	AUGMENT	0	49	1	4	5		
MATERIAL HANDLING	SUPP FUNC COMF	0	13	0	1	1		
	P25A	0	6	0	0	0		
	AUGMENT	0	0	0	0	0		

TRAINING REPORT

UNIT: NMCB SIXTY-TWO
REPORT FOR 26 MAY 1967 to 25 JUNE 1967

1. Training Conducted:

<u>Training Activity</u>	<u>Course or Lesson Subject</u>	<u>Duration</u>	<u>Number Attended</u>
Medical Dept.	Security Rock Quarry	40 Min.	26
Medical Dept.	Security Camp	30 Min.	33
Medical Dept.	Security Rock Quarry	30 Min.	18
Dental Dept.	General Dental Material	4 Hr.	3
Training Dept.	M-14 Range (Firing)	3 Hr.	25
Training Dept.	M-79 Range (Firing)	3 Hr.	25
Training Dept.	M-60 Range (Firing)	3 Hr.	25
Training Dept.	Hand Grenades (Live)	3 Hr.	25
Supply Dept.	Review of Material Cognizance	1 Hr.	10
Supply Dept.	Federal Catalog System	1 Hr.	10
Supply Dept.	Material Classification	1 Hr.	10
Supply Dept.	Cataloging Navy Items	1 Hr.	10
Supply Dept.	General Disbursing (Part II)	1 Hr.	4
Supply Dept.	General Disbursing (Part III)	1 Hr.	4
Supply Dept.	Travel & Per Diem (Part II)	1 Hr.	4
Supply Dept.	Travel & Per Diem (Part III)	1 Hr.	4
Supply Dept.	Ship Store Returns & Submis. of	1 Hr.	4
Supply Dept.	Operations of the Ret. Store	1 Hr.	4
Supply Dept.	Cash Register Record	1 Hr.	4
Supply Dept.	Cash Receipt Book	1 Hr.	4
Supply Dept.	Nutrition & Menu Planning	1 Hr.	5
Supply Dept.	Calories in Meal Planning	1 Hr.	5
Supply Dept.	Vitamins in Meal Planning	1 Hr.	5
Supply Dept.	Analyze Your Menu	1 Hr.	5
Supply Dept.	Percentage Mark-up in Sales of		
	Beef to Wardroom Mess	1 Hr.	12
Supply Dept.	Preparation of the S & A	1 Hr.	12
Supply Dept.	Operation of the Subsistence		
	Expenditure Log	1 Hr.	12
Supply Dept.	Breakouts to the Gen. Mess	1 Hr.	12

2. Correspondence Courses and Extension Courses:

	<u>Enrolled</u>	<u>Completed</u>
a. Officer Courses	3	0
b. Enlisted Courses	32	52
c. USAFI	0	0

3. Examinations Administered:

Enclosure (3)

a. USAFI/GED ECT. 13

b. Advancement in Rate 7.

E-3 - 6

O-3 - 1

LABOR DISTRIBUTION REPORT

UNIT NMCB 62 PERIOD ENDING 25 JUNE 1967

WORK DAYS THIS PERIOD-- <u>26</u> -- NMCB AVG ON BOARD PERSONNEL AT EMPLOYMENT SITE <u>756</u>	MANDAYS			PERCENT TOTAL UNIT LABOR AVAILABLE
	UNIT	OTHER	TOTAL	
DIRECT LABOR				
TOTAL CI DIRECT LABOR				
TOTAL FILL-IN DIRECT				
TOTAL DIRECT LABOR	9446		10,744	49.4%
INDIRECT LABOR				
X01 CONST EQUIP MAINT REPAIR AND RECORDS	2024		2024	
X02 OPERATIONS AND ENGINEERING	646		646	
X03 PROJECT SUPERVISION	765		765	
X04 PROJECT EXPEDITING (SHOP PLANNER)	29		29	
X05 LOCATION MOVING	2		2	
X06 PROJECT MATERIAL SUPPORT	414		414	
X07 TOOL AND SPARE PARTS ISSUE	303		303	
X08 OTHER	144		144	
TOTAL INDIRECT LABOR	4327		4327	19.9%
MILITARY OPERATIONS AND READINESS				
M01 MILITARY OPERATIONS	1652		1652	
M02 MILITARY SECURITY				
M03 EMBARKATION				
M04 UNIT MOVEMENT				
M05 MOBILITY PREPARATION				
M06 CONTINGENCY MATERIAL READINESS	197		197	
M07 MILITARY ADMINISTRATIVE FUNCTIONS				
M08 MOBILITY & DEFENSE EXERCISES				
M09 OTHER				
TOTAL MILITARY OPS AND READ	1849		1849	7.3%

Enclosure (4)

	MANDAYS		PERCENT TOTAL UNIT LABOR AVAILABLE
	UNIT	OTHER	
DISASTER RECOVERY OPERATIONS			
DO1 DISASTER RECOVERY OPS			
DO2 DISASTER RECOVERY EXERCISES			
TOTAL DISASTER RECOVERY OPS			
TRAINING			
TO1 TECHNICAL TRAINING	75		75
TO2 MILITARY TRAINING			
TO3 DISASTER RECOVERY TRAINING			
TO4 LEADERSHIP TRAINING			
TO5 SAFETY TRAINING			
TO6 TRAINING ADMIN	88		88
TOTAL TRAINING LABOR	163		163
			0.8%
TOTAL PRODUCTIVE LABOR			
OVERHEAD LABOR			
YO1 ADMIN & PERSONNEL	604		604
YO2 MEDICAL AND DENTAL DEPTS	296		296
YO3 SHIP SERVICE & SPECIAL SERVICES	160		160
YO4 SUPPLY & DISBURSING	479		479
YO5 COMMISSARY	1416		1416
YO6 CAMP UPKEEP & REPAIR	720		720
YO7 SECURITY	405		405
YO8 LEAVE & LIBERTY	669		669
YO9 SICKCALL, DENTAL & HOSPITALIZATION	112		112
YO10 PERSONAL AFFAIRS	50		50
YO11 LOST TIME	53		53
YO12 TAD NOT FOR UNIT	33		33
YO13 OTHER	1		1
TOTAL OVERHEAD LABOR	4998		4998
			22.5%
TOTAL LABOR AVAILABLE	22081		22081
			100%

FISCAL SUMMARY OF CONSTRUCTION OPERATIONS

UNIT: NMCB SIXTY-TWO

PERIOD ENDING 25 JUNE 1967

DURING REPORTING PERIOD DEPLOYMENT TO DATE

PROJECT SUPPORT COSTS
(BP 40 MILCON)

\$1,599.50

\$4,229.69

PROJECT EQUIPMENT
SUPPORT COSTS
(BP 68 AUTOMOTIVE)

\$38,427.23

\$249,068.75

PROJECT MATERIAL
IN PLACE

\$121,771.02

\$1,358,069.27

FISCAL SUMMARY OF CONSTRUCTION OPERATIONS

UNIT: NMCB SIXTY-TWO

PERIOD ENDING 25 JUNE 1967

DURING REPORTING PERIOD DEPLOYMENT TO DATE

PROJECT SUPPORT COSTS
(BP 40 MILCON)

\$1,599.50

\$4,229.69

PROJECT EQUIPMENT
SUPPORT COSTS
(BP 68 AUTOMOTIVE)

\$38,427.23

\$249,068.75

PROJECT MATERIAL
IN PLACE

\$121,771.02

\$1,358,069.27

PROGRESS PHOTOGRAPHS

CAPTION PAGE FOR 8" X 10" BLACK AND WHITE PHOTOGRAPHS

1. 6DSA87222A. FLSG/A Fencing. Delta Company stretching wire fabric for FLSG/A perimeter fence.
2. 6DCA84102A. Water Supply, Phu Bai. Construction of dam for water storage for Phu Bai Water.
3. 6DCA84102A. Water Supply, Phu Bai.
Top Left - Pump House exterior.
Top Right - Interior Pump House
Bot Left - Main treatment (settling) tank
Bot right - 500 bbl storage and pressure tower in 3rd Mar Div area.
4. 7XXX05229E. Phu Bai Airfield Rehabilitation. Hand spraying the final section of the runway/taxiway/parking apron seal coat job.
5. 6DSA81209. Power Distribution, Phu Bai. Most of the wire is now strung and all of the transformers are set.
6. 6DSA81209. Power Distribution, Phu Bai. Setting the first 700 KW Muse Generator (90,000 pounds).
7. 6DBA85102. 3rd Marine Division Roads. Compacting 18" laterite base for "H" road.
8. 6DBA85102. 3rd Marine Division Roads. Spreading 6" rock wearing wearing course prior to application of RC-800 and fines.
9. MCB 62-221E. 3 SATS Hangars for MAG-16. Building being erected without re-erection kit; bolts, welding, and TEK fasteners replace self expanding rivets.
10. 6DBX11301A. VMO Parking Apron. Making joint repairs to soil-cement apron.
11. FSI 7-01. Hue Interrogation Center. Crane is setting cell block and cell doors. Ready for placement of bond beam.
12. 6AFA44204A. 3rd Marine Division, 18RF buildings. Placing deck in buildings 30 and 31.
13. 6DDA21001A. 3rd Mar Div, 4RF Shop buildings. The vault on Disbursing building was formed and placed.
14. 6LZZ00050D. Route 1 Improvement. Patching potholes.
15. 6ADA21111A. 3rd Mar Div, 4RF Shops. Erecting steel for the 3rd Tank Battalion Maintenance Shop.
16. XXX00004E. Mag 16 Well.
17. 6DTA72501A. & 6DTA80103A. 131ST Aviation Company Generator Shed and Boiler House for galley equipment installation.
18. 6DSA45417. FLSG/A Optical Shop
19. And worth every penny of it!

Enclosure (8)



U. S. Naval Mobile Construction Battalion
Sixty-Two, FPO New York

Official U. S. Navy Photo
Not for Publication unless Officially released

MCB-62-1460-6-67
6-22-67

Proj. No. 6DSA87222A
Phu Bai, Vietnam

Delta Company stretching wire fabric for FLSG/A
perimeter fence.






U. S. Naval Mobile Construction Battalion
Sixty-Two, FPO New York

Official U. S. Navy Photo
Not for publication unless Officially released

MCB-62-1399-6-67
6-24-67

Project No. 6DCA84102A
Phu Bai, Vietnam

Construction of dam for water storage for Phu Bai
water.

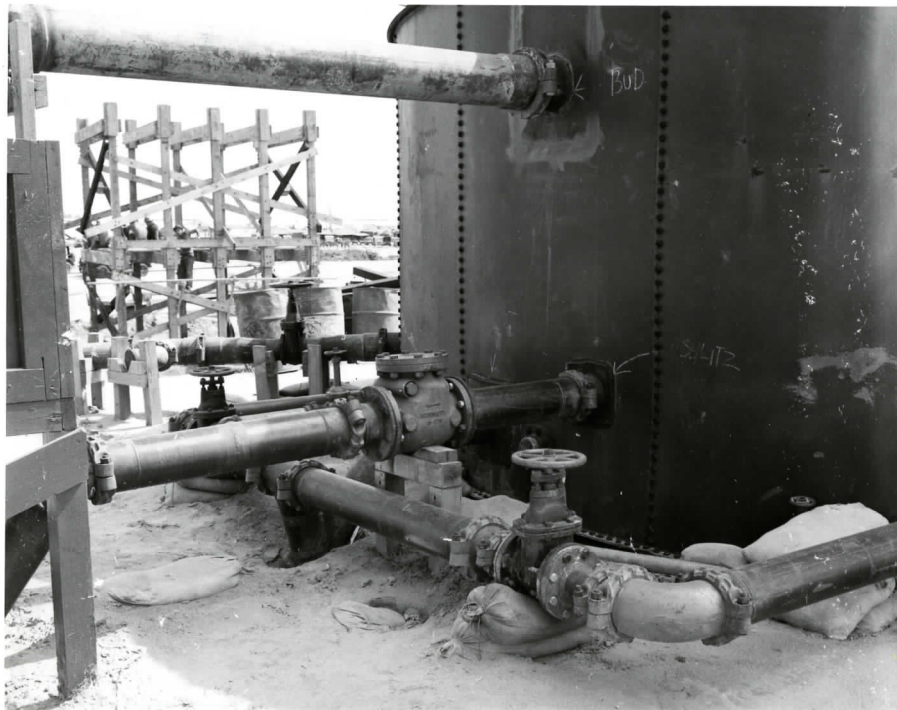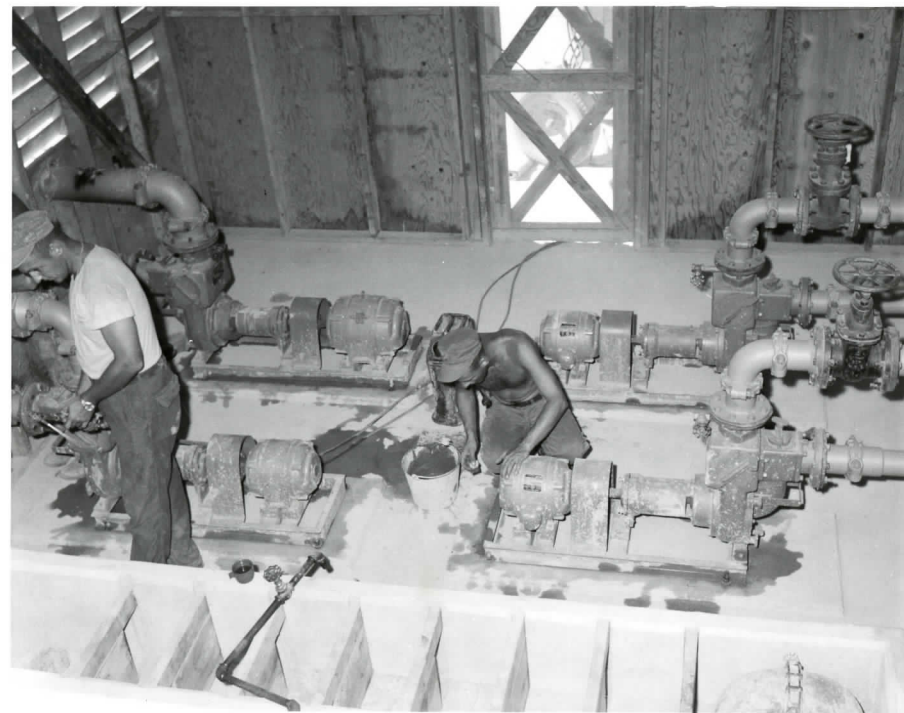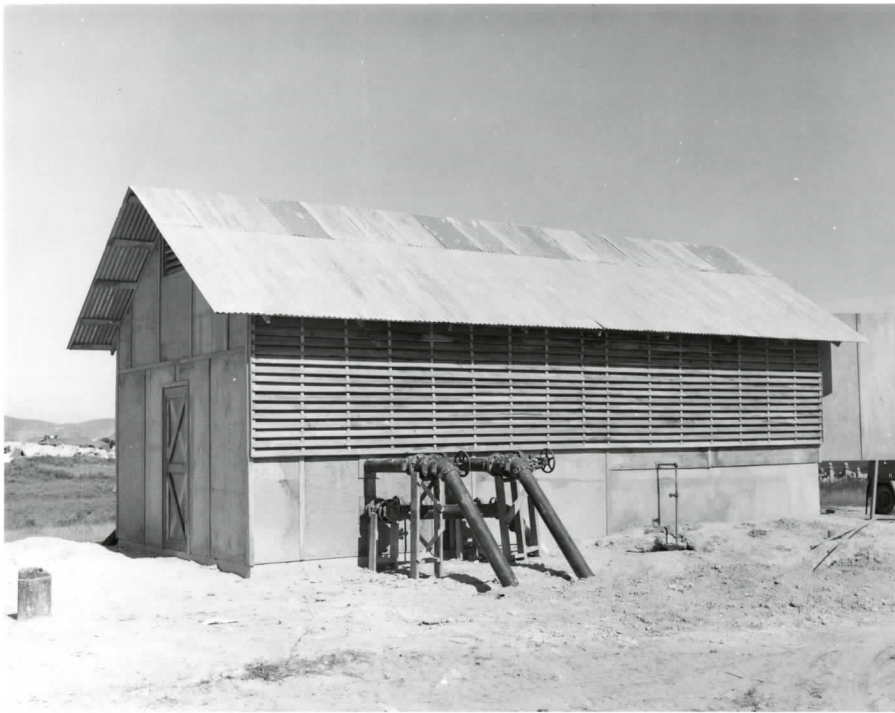

U. S. Naval Mobile Construction Battalion
Sixty-Two, FPO New York

Official U. S. Navy Photo
Not for publication unless Officially released

TL (MCB-62-1426-6-67)	Project No. 6DCA84102A
BL (MCB-62-1419-6-67)	Phu Bai, Vietnam
TR (MCB-62-1421-6-67)	5-25-67
BR (MCB-62-1424-6-67)	

TL-Pump House exterior, BL-Main Treatment (settling)
tank, TR-Interior Pump House, BR-500 HBL Storage and
pressure tower in 3rd Mar Div area




U. S. Naval Mobile Construction Battalion
Sixty-Two, FPO New York

Official U. S. Navy Photo
Not for publication unless Officially released

MCB-62-1366-6-67
6-20-67

Project No. 7XXX05229E
Phu Bai, Vietnam

Hand spraying the final section of the runway/taxiway/
parking apron seal coat job.

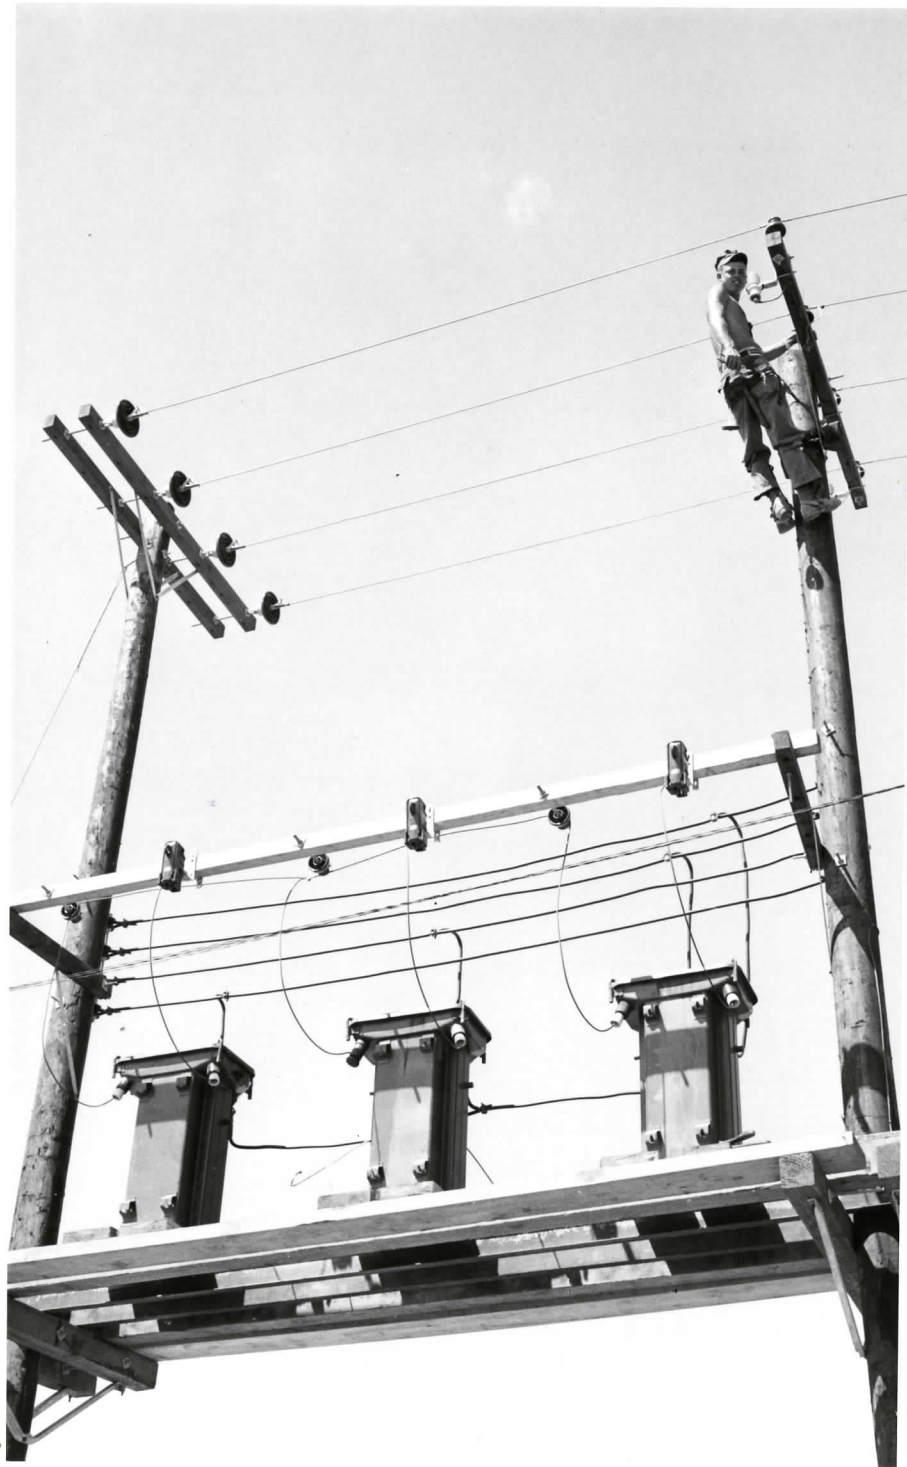

U. S. Naval Mobile Construction Battalion
Sixty-Two, FPO New York

Official U. S. Navy Photo
Not for publication unless Officially released

L(MCB-62-1450-6-67)

R(MCB-62-1448-6-67)

6-20-67

Project No. 6DSA81209
Phu Bai, Vietnam

Most of the wire is now strung and all of the
transformers are set.



U. S. Naval Mobile Construction Battalion
Sixty-Two, FPO New York

Official U. S. Navy Photo
Not for publication unless Officially released

MCB-62-1453-6-67
6-26-67

Project No. 6DSA81209
Phu Bai, Vietnam

Setting the first 700 KW Mase Generator (90,000 lbs.)



U. S. Naval Mobile Construction Battalion
Sixty-Two, FPO New York

Official U. S. Navy Photo
Not for publication unless Officially released

MCB-62-1465-6-67
6-24-67

Project No. 6DBA85102
Phu Bai, Vietnam

Compacting 16" laterite base for "H" road.



U. S. Naval Mobile Construction Battalion
Sixty*Two FPO New York

Official U. S. Navy Photo
Not for publication unless Officially released

MCB-62-1466-6-67
6-26-67

Project No. ODBA85102
Phu Bai, Vietnam

Spreading 6" rock wearing course prior to application
of RC-800 and fines.



U. S. Naval Mobile Construction Battalion
Sixty-Two, FPO New York

Official U. S. Navy Photo
Not for publication unless Officially released

MCB-62-1359-6-67
6-22-67

Project No. MCB 62-221E
Phu Bai, Vietnam

Building being erected without re-erection kit; bolts,
welding, and TEK fasteners replace self expanding rivets.




U. S. Naval Mobile Construction Battalion
Sixty-Two, FPO New York

Official U. S. Navy Photo
Not for publication unless Officially released

MCB-62-1363-6-67
6-26-67

Project No. 6DBX11301A
Phu Bai, Vietnam

Making joint repairs to soil cement apron.

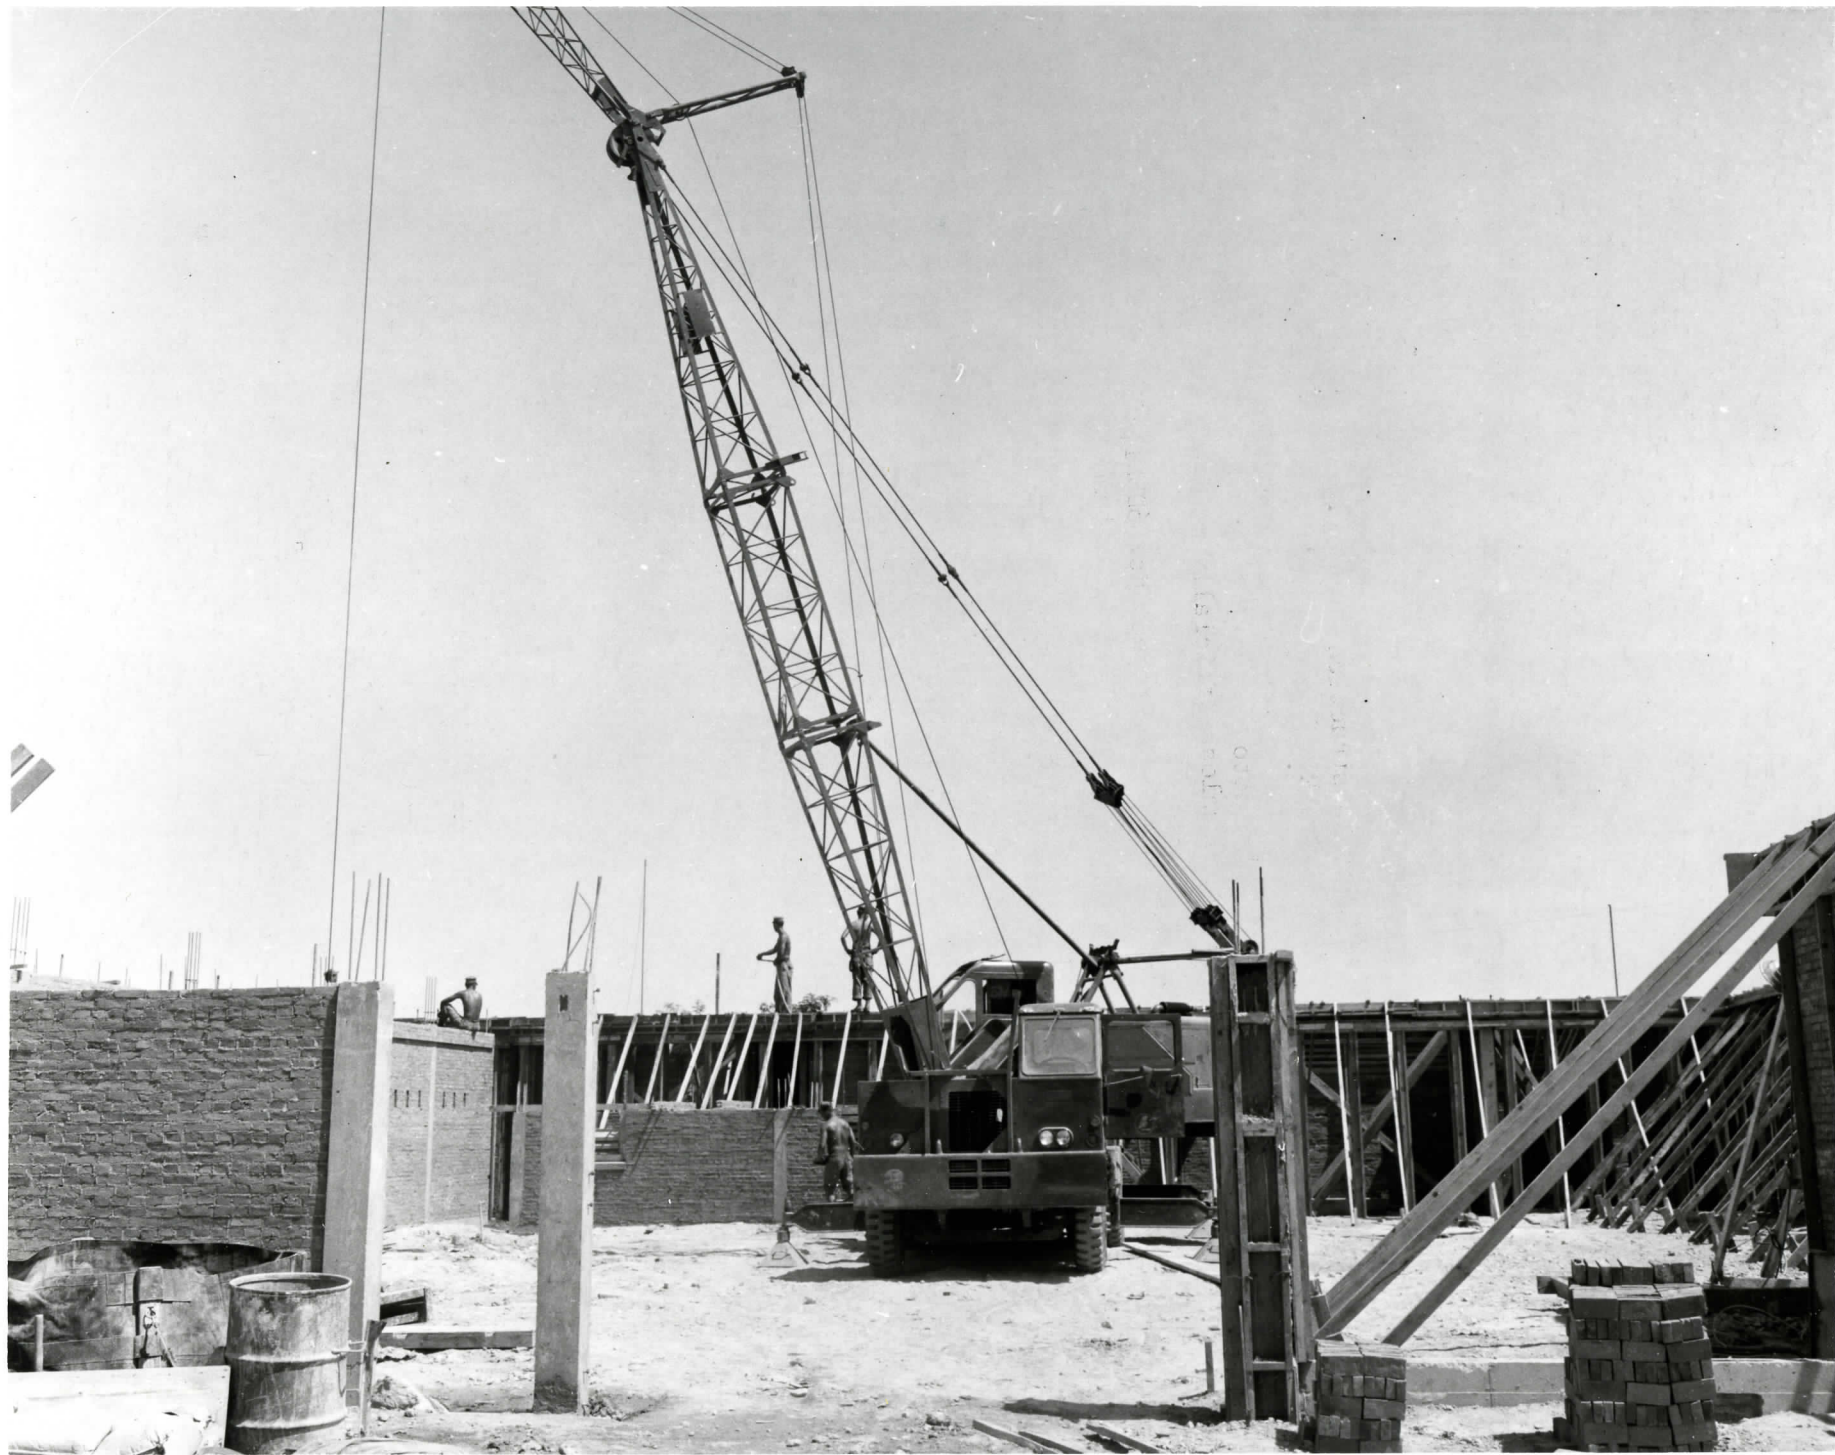

U. S. Naval Mobile Construction Battalion
~~Sixty-Two~~, FPO New York

Official U. S. Navy Photo
Not for publication unless Officially released

MCB-62-1361-6-67
6-26-67

Project No. FSI 7-01
Phu Bai, Huo, Vietnam

Crane is setting cell block and cell doors. Ready for
placement of bond beams.




U. S. Naval Mobile Construction Battalion
Sixty-Two, FPO New York

Official U. S. Navy Photo
Not for publication unless Officially released

MCB-62-1429-6-67
6-14-67

Project No. 6AFAL4204A
Phu Bai, Vietnam

Placing deck in buildings 30 and 31.

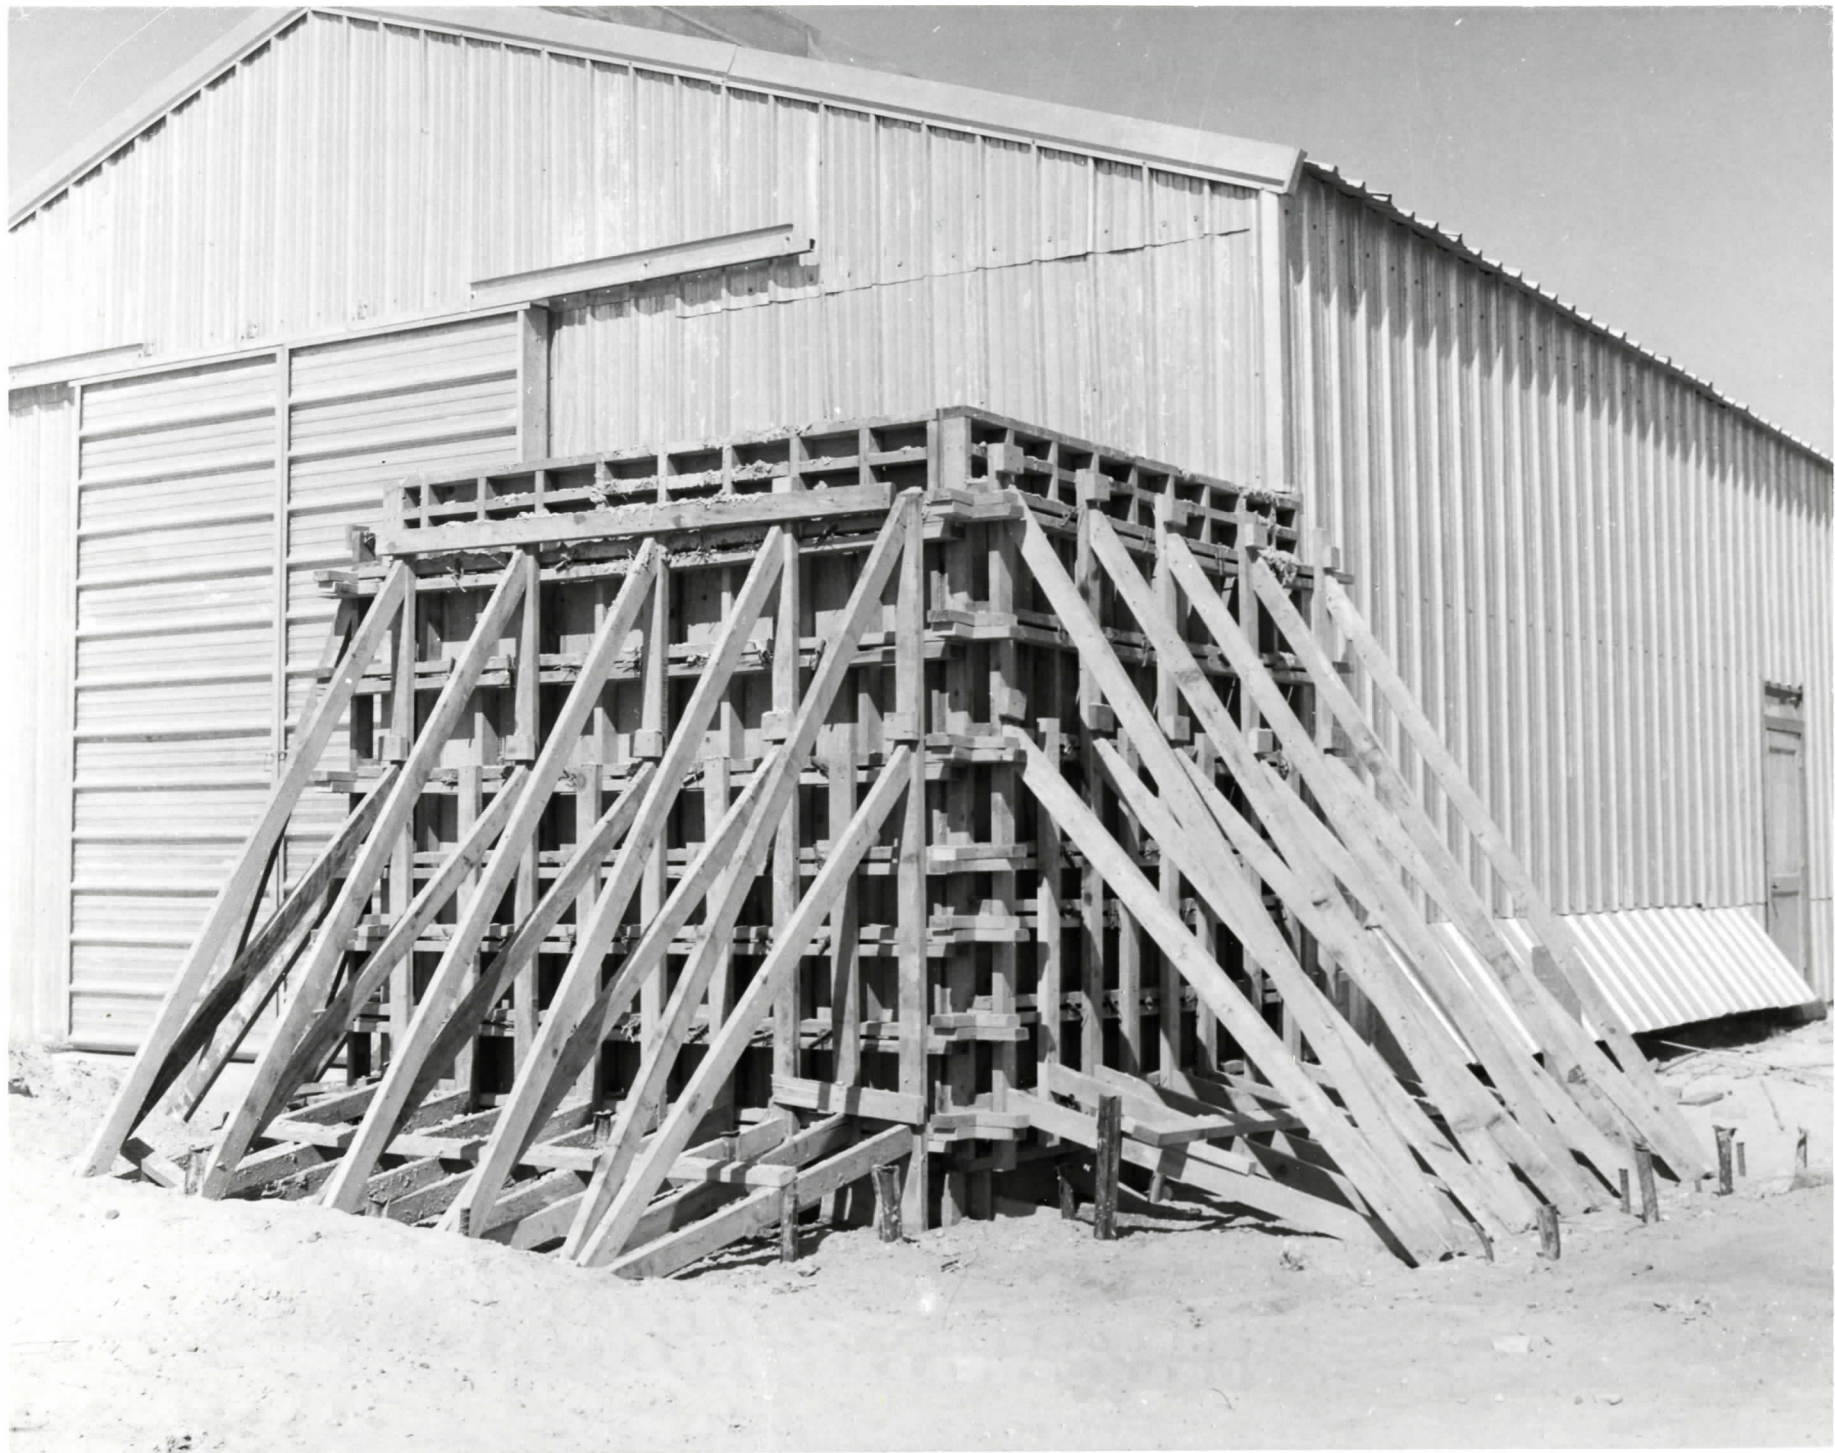

U. S. Naval Mobile Construction Battalion
Sixty-Two, FPO New York

Official U. S. Navy Photo
Not for publication unless Officially released

MCB-62-1425-6-67
6-20-67

Project No. 6DDA21001A
Phu Bai, Vietnam

The vault on Disbursing Building was formed and placed.



U. S. Naval Mobile Construction Battalion
. Sixty-Two, FPO New York


Official U. S. Navy Photo
Not for publication unless Officially released.

MCB-62-1372-6-67
6-14-67

Project No. 6LZZ00050D
Phu Bai, Vietnam

Patching Potholes.



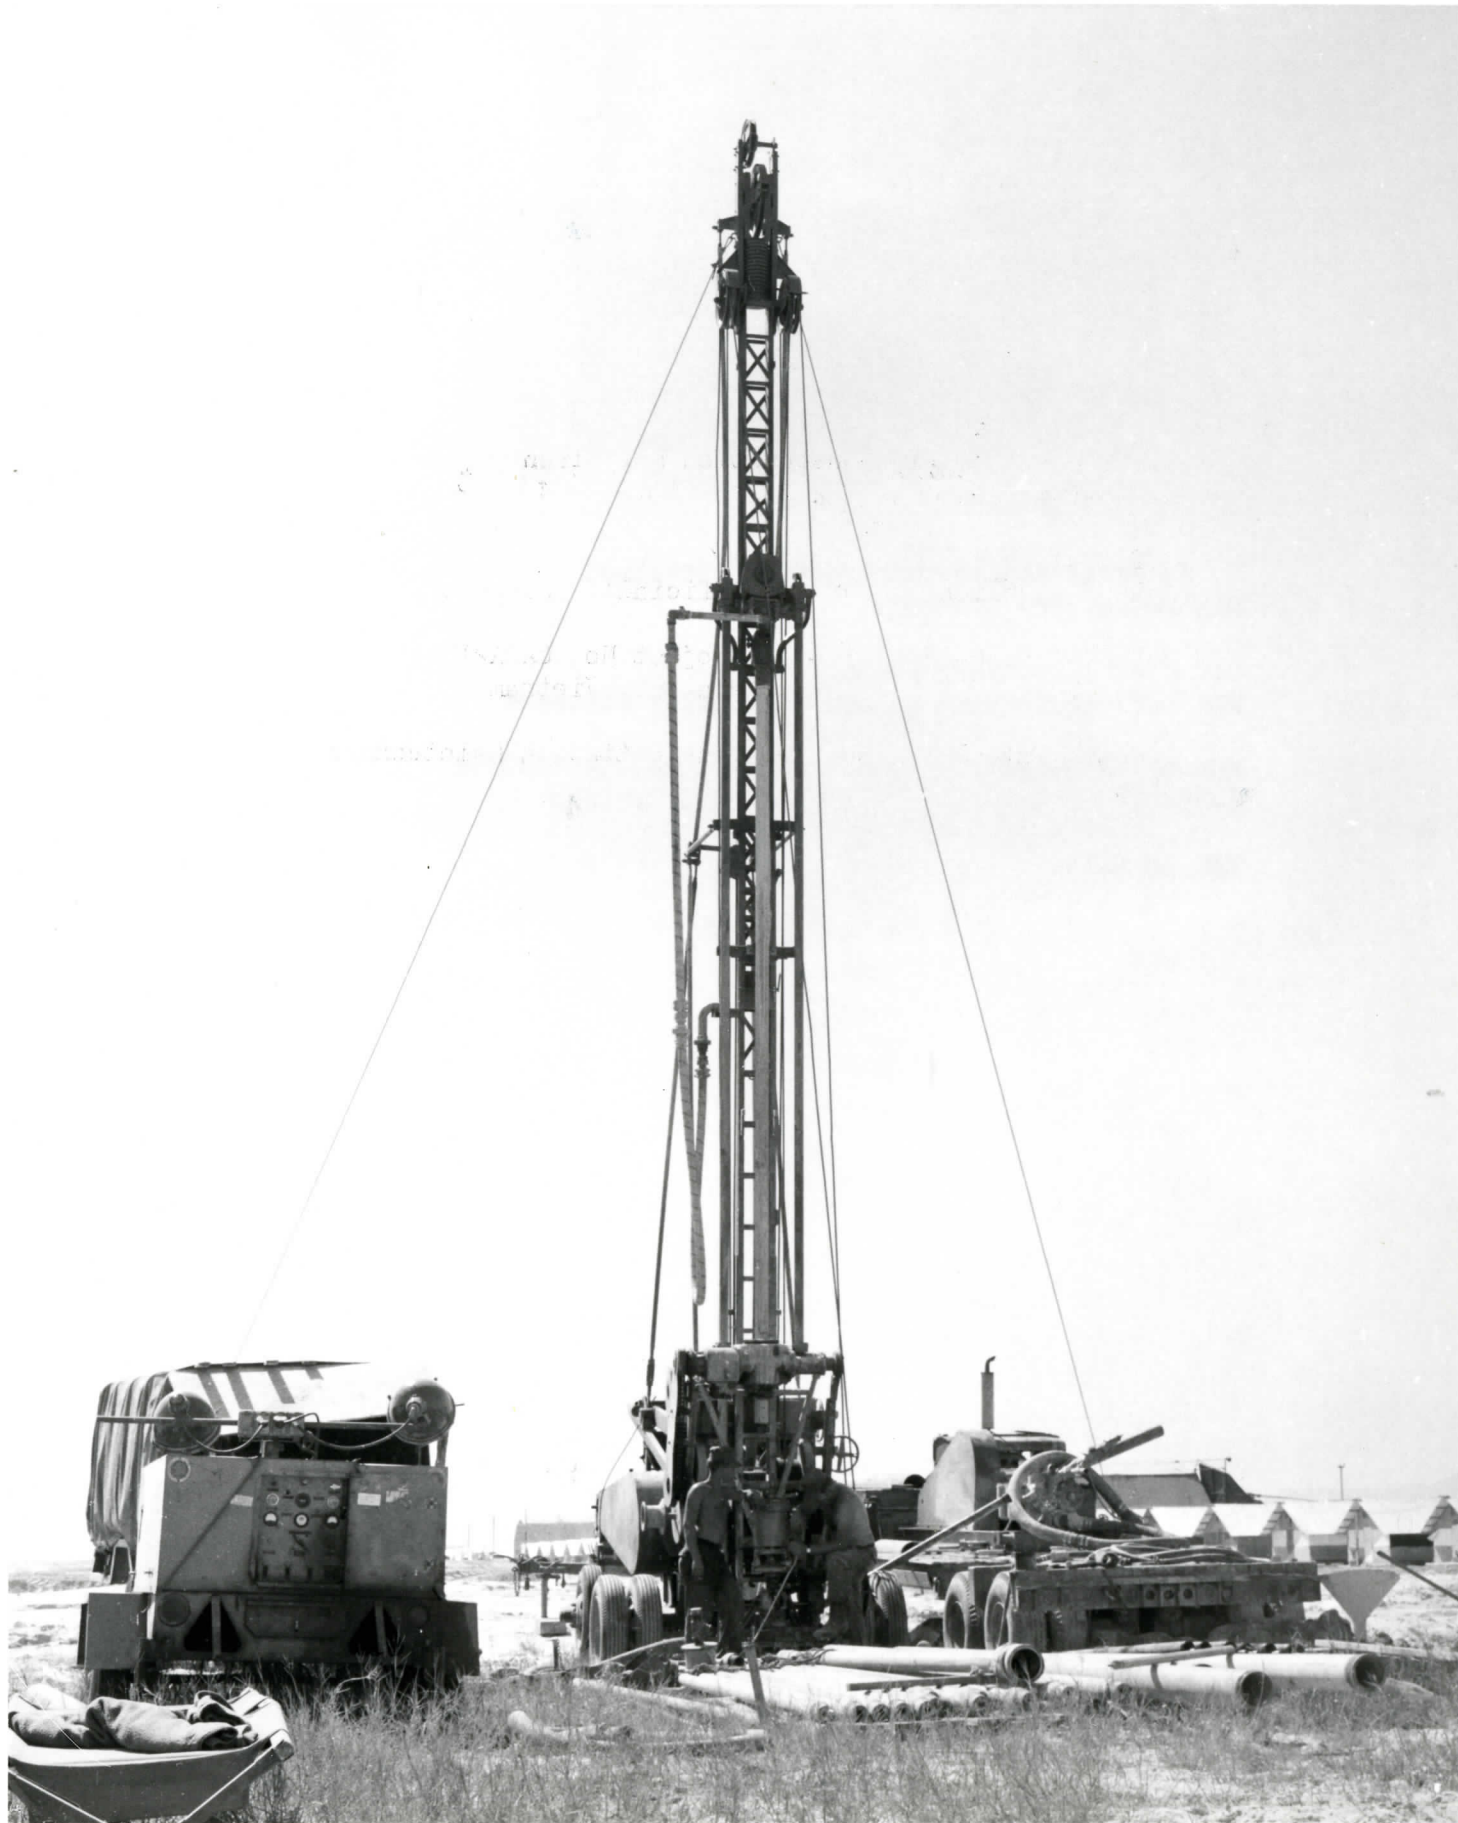


U. S. Naval Mobile Construction Battalion
Sixty-Two, FPO New York

Official U. S. Navy Photo
Not for publication unless Officially released

MCB-62-1368-6-67
6-25-67

Project No. 7XXX00004E
Phu Bai, Vietnam

MAG 16 Well..

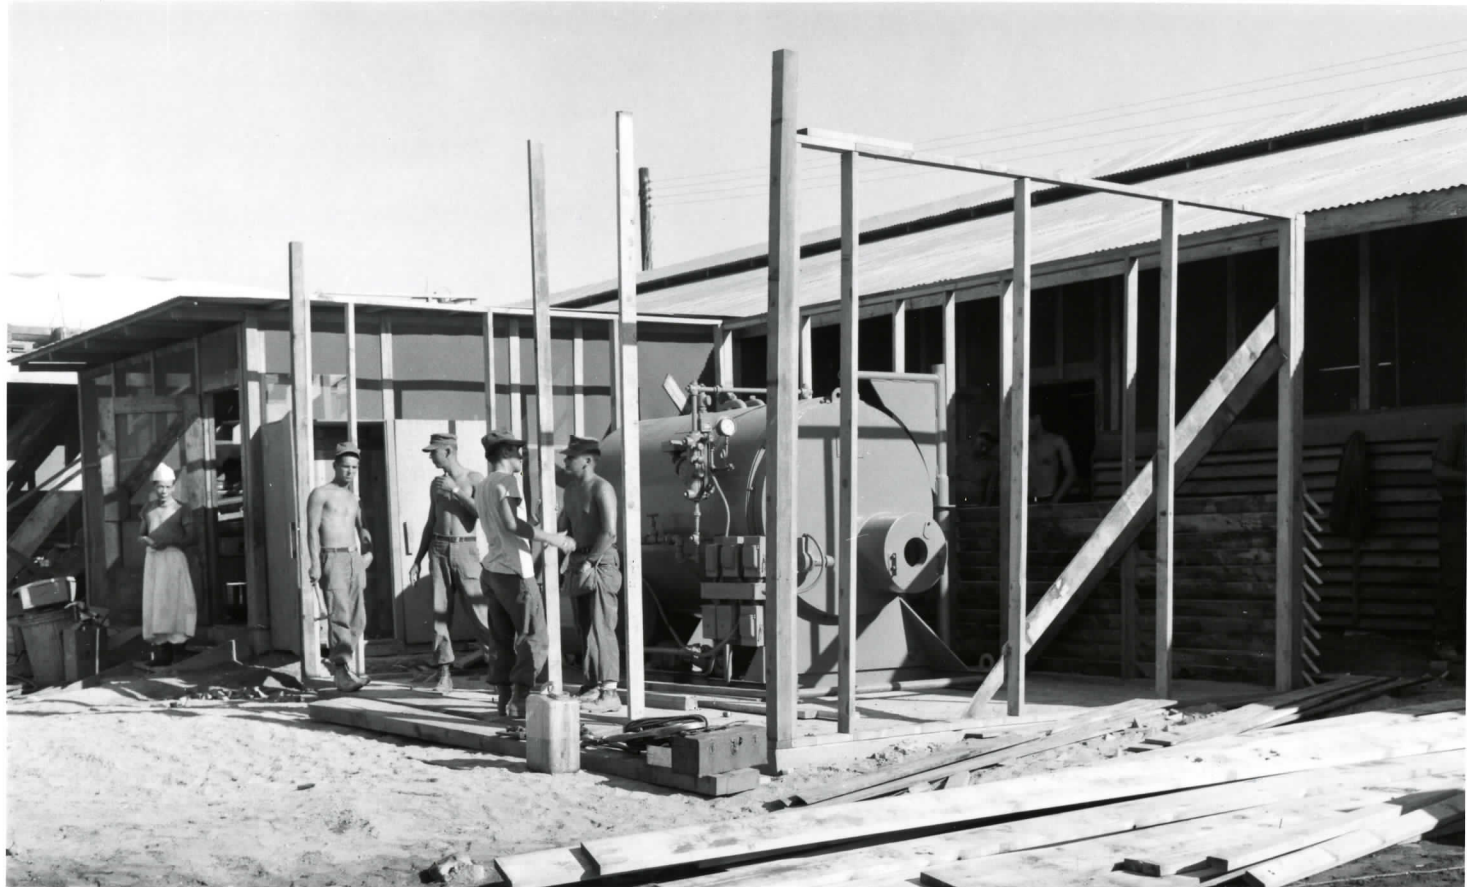

U. S. Naval Mobile Construction Battalion
Sixty-Two, PPO New York

Official U. S. Navy Photo
Not for publication unless Officially released

MCB-62-1428-6-67	TOP	Project No. 7DTA72501A &
MCB-62-1427-6-67	BOT	6DTA80103A
6-18-67		Phu Bai, Vietnam

131st Aviation Company Generator Shed and Boiler House
for galley equipment installation.



U. S. Naval Mobile Construction Battalion
Sixty-Two, FPO New York

Official U. S. Navy Photo
Not for publication unless Officially released

MCB-62-1369-6-67
6-16-67

Project No. 6DSA45417
Phu Bai, Vietnam

FLSG/A Optical Shop



THIS EQUIPMENT
COST 2,300.00

U. S. Naval Mobile Construction Battalion
Sixty-Two, FPO New York

Official U. S. Navy Photo
Not for publication unless Officially released

MCB-62-1376-6-67
6-20-67

Project No.
Phu Bai, Vietnam

And worth every penny of it!
